Project Monitoring System

Reference Manual for Maintaining MOFPI projects

Released on: May 2011

Brought to you by
Ministry Of Food Processing Industries
New Delhi, INDIA

Table of Contents

Section	Page Number
1) Introduction	3
2) Login Page	4
3) Home page for Administrator	5
4) Manage Projects-Add New Project	12
5) Update Project Detail	28
6) PERT Chart	32
7) SMS & Email Communication	40
8) Manage Masters	43

User Manual for MOFPI web application

Introduction:

This Web application helps the Ministry of Food Processing Industries (MOFPI) Officials to manage and maintain the details of various projects under different project schemes. A New project detail can be added, existing project can be modified using the application. The major activities (milestones) in the project can be monitored using PERT charts and the time taken to complete the milestone can be found.

The map in the home page shows the locations of various projects. There are various graphs which show the project progress status, projects summary, grants release status etc which will provide an overview of the projects under MOFPI.

Login Page

The MOFPI users can log into the system using the User ID and password credentials provided by the MOFPI system administrator.

Users are grouped into different user types. The Home page and accessible features of the system depends on the type of user logged in.

Project Monitoring System
Ministry of Food Processing Industries
Today's : 2/6/2011 02:50:15 PM
MOFPI
Login
Effective utilization of resources and monitoring of projects is going....
User ID
Password
Login
Overview
Scheme Guidelines
MOFPI Grants
Milestones & Activities
Approved Projects
Agencies to Contact
Overview
The food processing sector is highly fragmented industry, it widely comprises of the following sub-segments: fruits and vegetables, milk and milk products, beer and alcoholic beverages, meat and poultry, marine products, grain processing, packaged or convenience food and packaged drinks. A huge number of entrepreneurs in this industry are small in terms of their production and operations, and are largely concentrated in the unorganized segment. This segment accounts for more than 70% of the output in terms of volume and 50% in terms of value. Though the organized
Mega Food Park
Abattoir
Cold Chain
Copyright @ 2011 | Ministry of Food Processing Industries, Government of India
Powered by Logicsoft

Home Page for Administrator

The Administrators can add a new project detail for any scheme; update the details of an existing project, View the Pert chart etc. All the features are explained in the following sections of this document.

The Home page for administrator is as shown in the screen below.

Click on the 'Map' link. All the locations of the projects under MOFPI can be found.

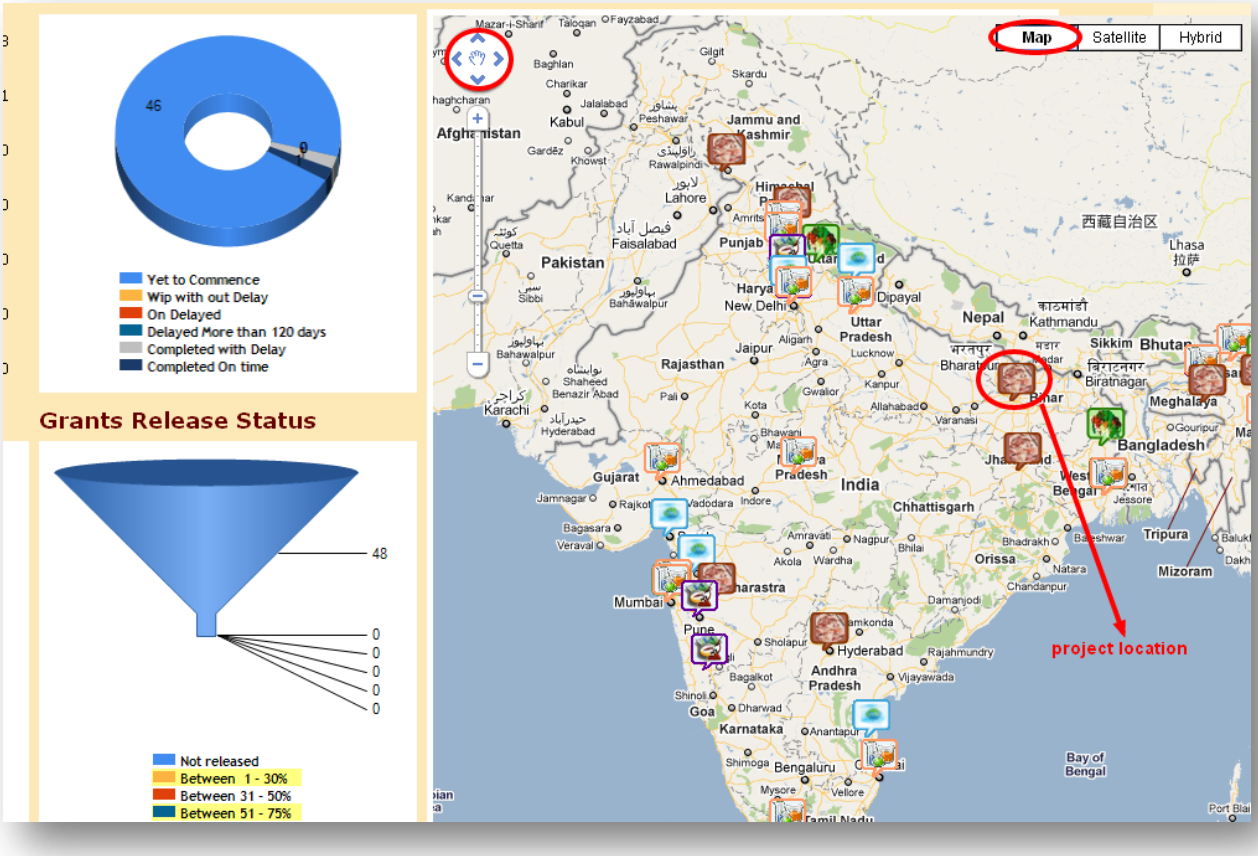

Click on any project location and a pop up will appear with the information about the project.

Click on the project name to find the summary of the project.

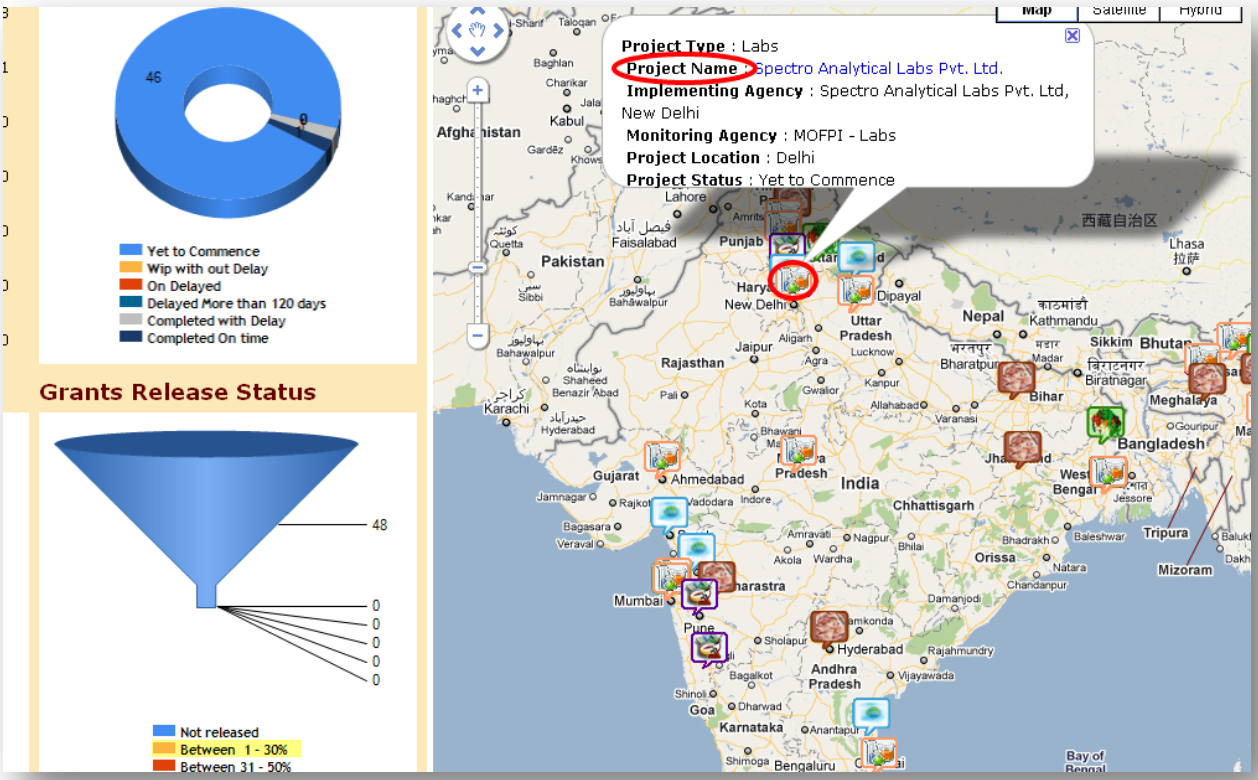

There is a filter in the Map tool to search the project locations based on the Scheme type. Select the scheme type and find all the projects under that scheme.

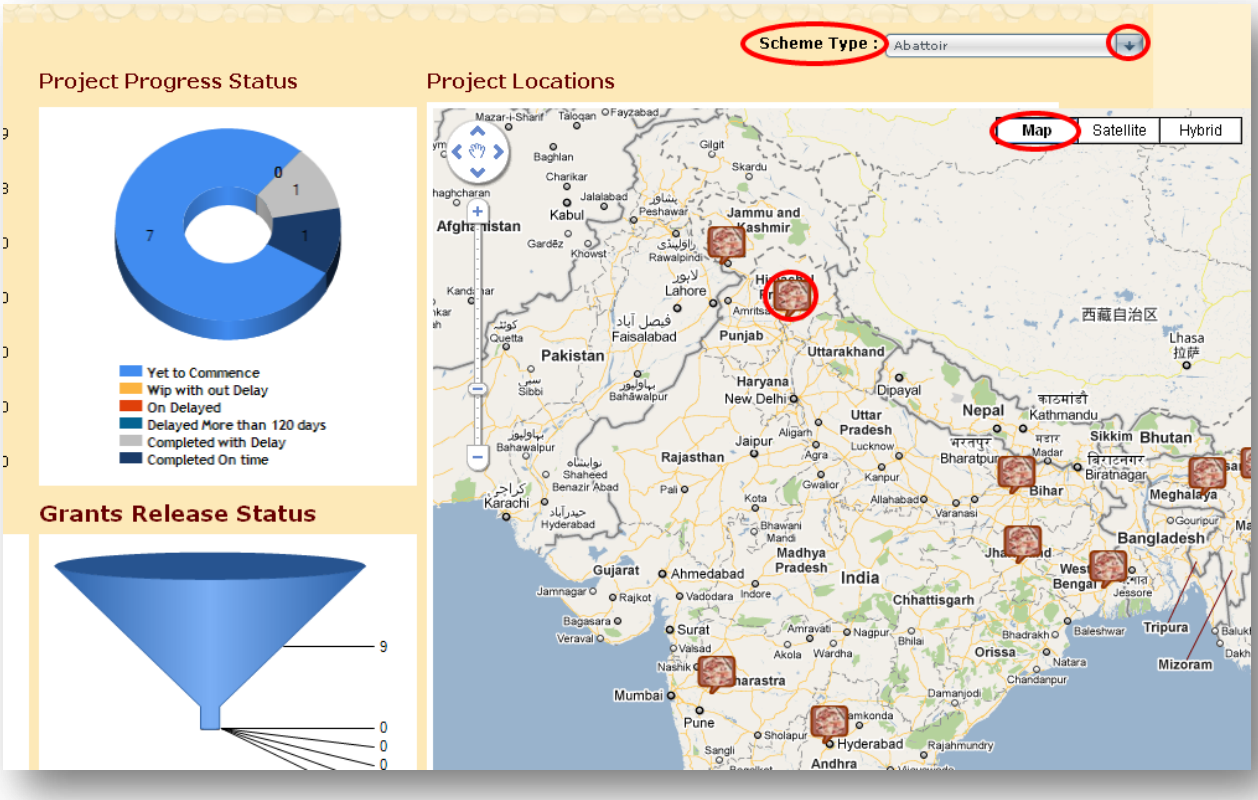

The Project locations can be found by using the ‘satellite’ or ‘Hybrid’.

Satellite Image

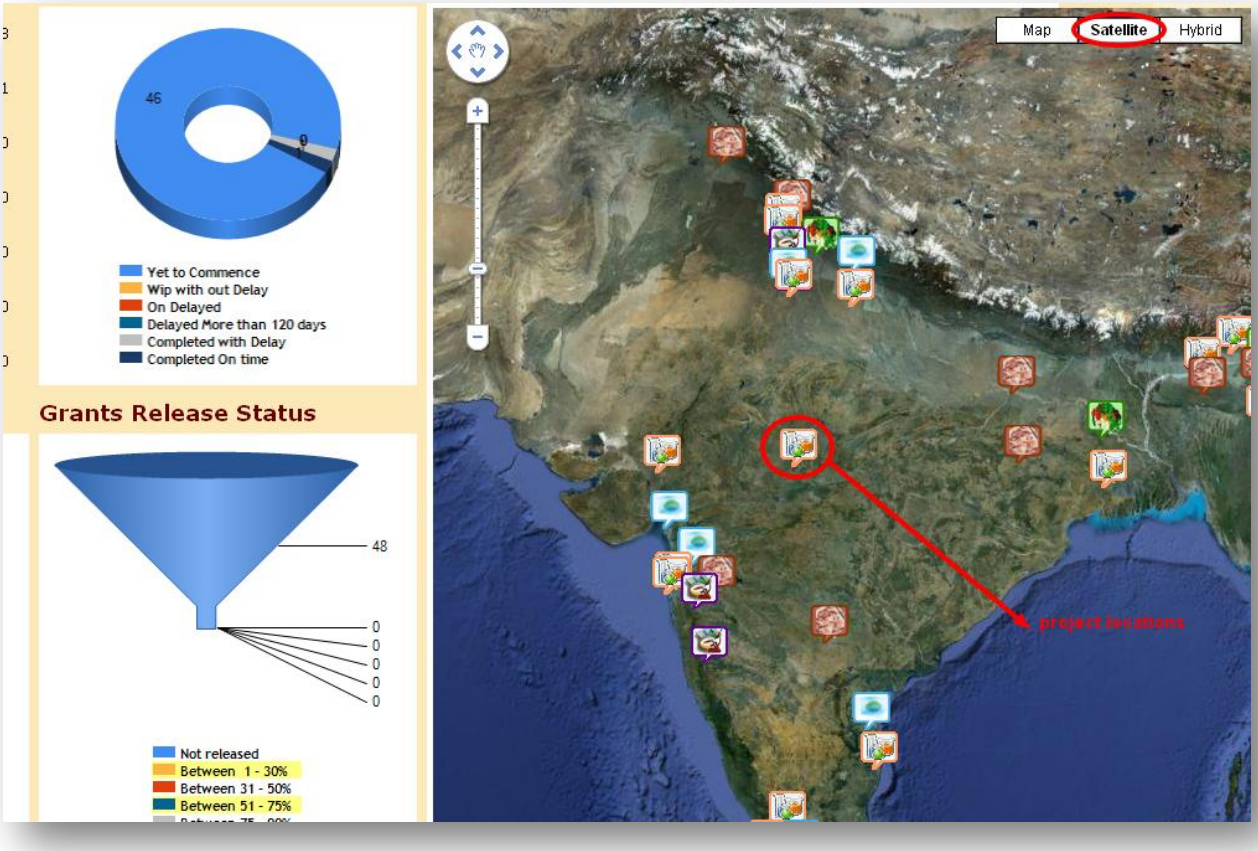

Hybrid Image

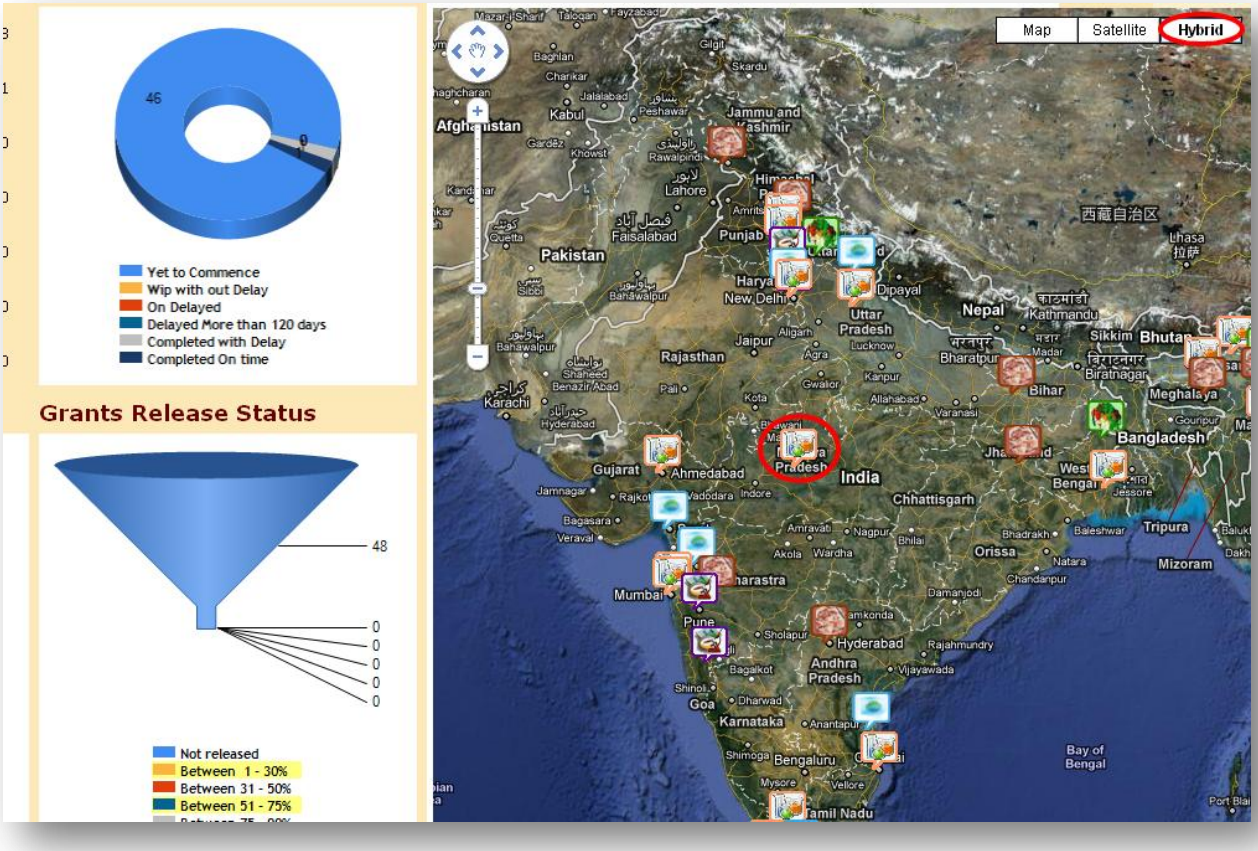

Other Charts

The Charts in this page will give the statistical data about the projects. It contains details like those given below.

1)Total Number of Projects

2)Updated within last One Month

3)No update for last Six Months

4)No update for last One Year

5)No. of Projects running delayed

6)No. of Projects due for payment

7) No. of Projects near completion.

These are dynamic data fetched from the database and will give the latest figures which can be used as a report.

Submission Status

Total Number of Projects	48
Updated within last One Month	11
No update for last Six Months	0
No update for last One Year	0
No. of Projects running delayed	0
No. of Projects due for payment	0
No. of Projects near completion	0

Project Progress Status

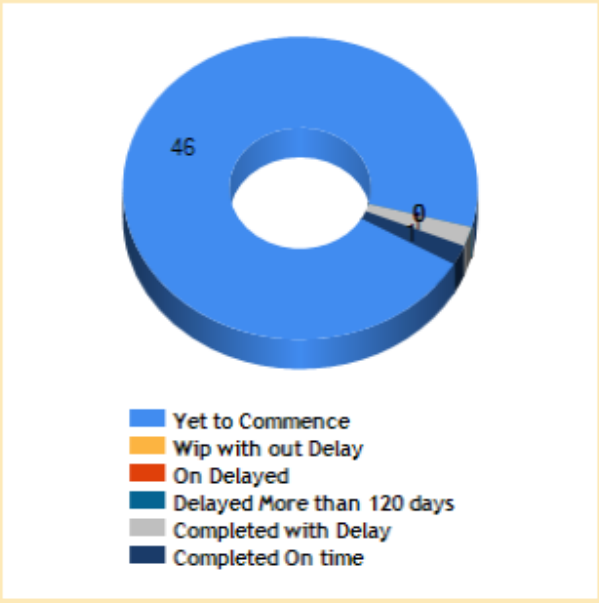

Projects Summary

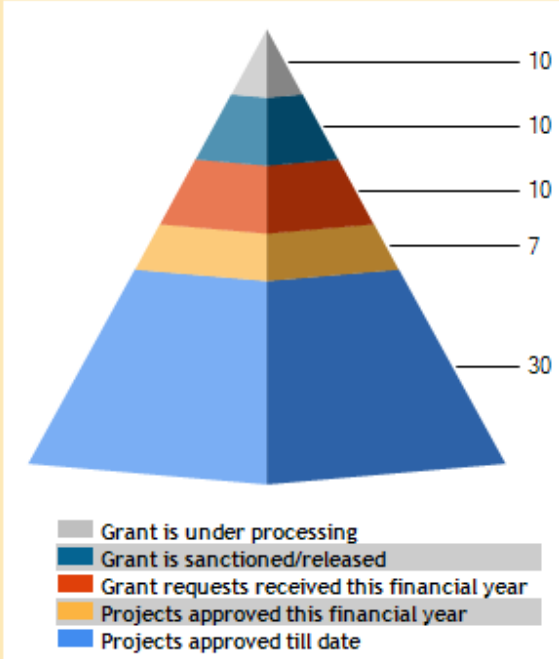

Grants Release Status

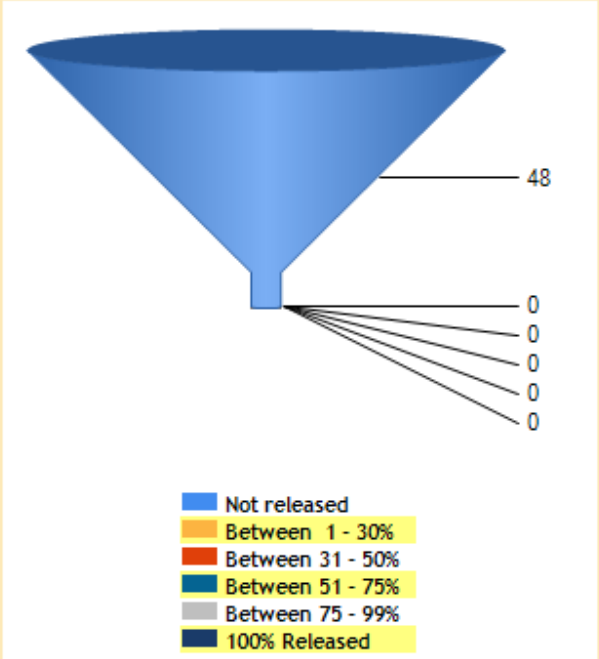

Manage Projects-Add New Project

To add the details of a new project find the new Project form. Move the mouse over ‘Manage Projects’ and click on ‘Add New Project’.

The Implementing agency (The agency executing the project) has to file an application (properly filled application form with supporting documents) to MOFPI (Ministry Of Food Processing Industries). After verifying the physical form details and documents, the MOFPI Officer can approve the application. After approval, the application details should be entered in the ‘New Project’ form as explained in the following section.

New project form

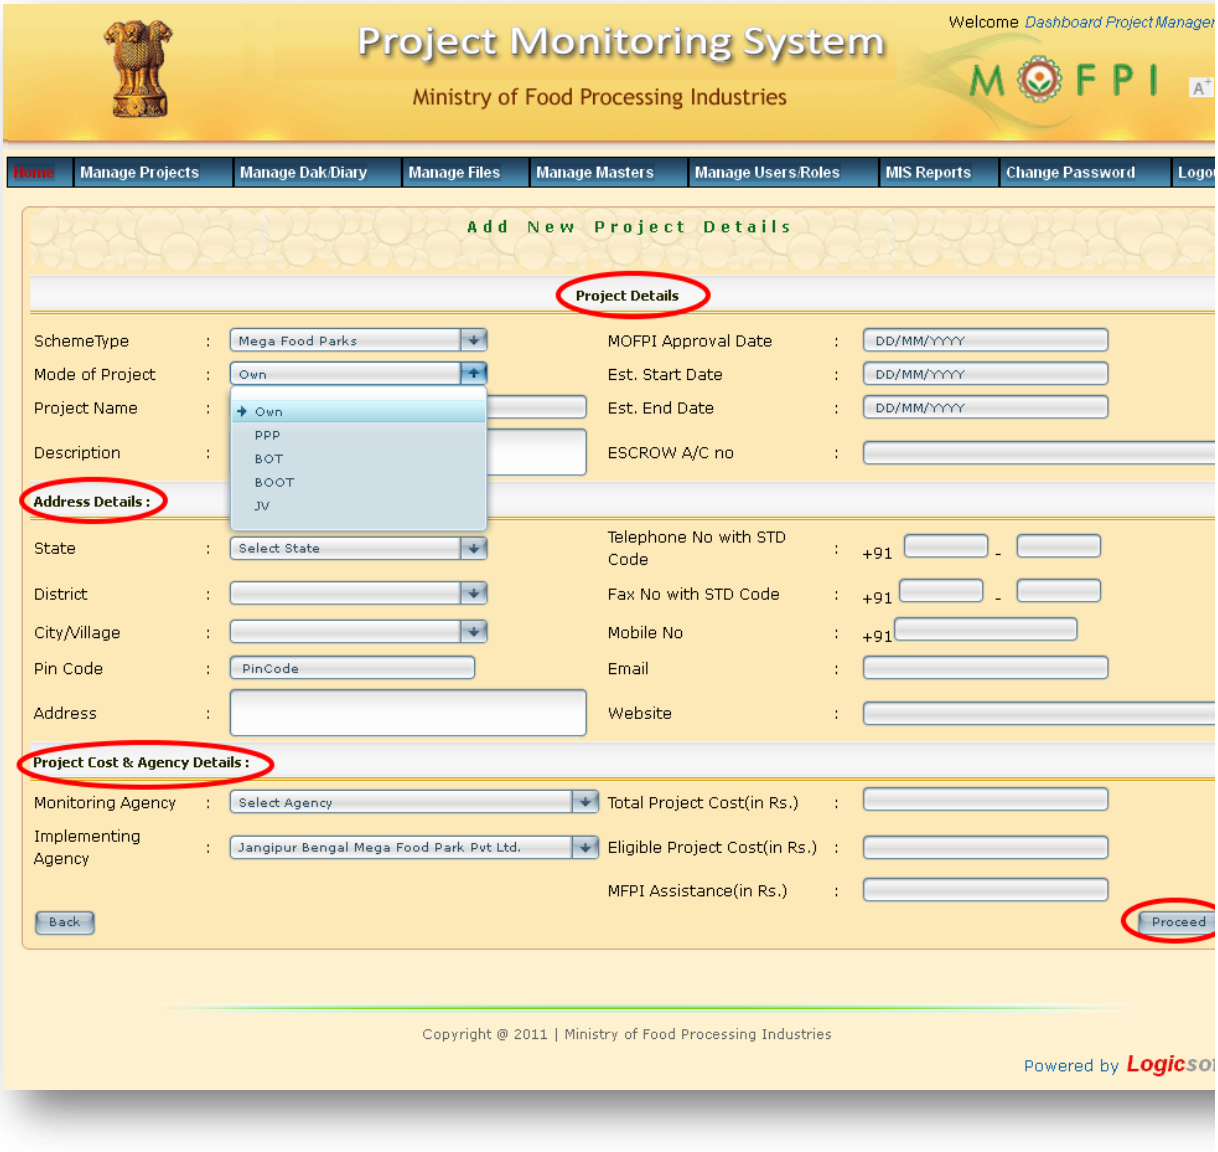

The different sections in the new project application form with the fields in each section are given below.

1.) Project details:-

Fields in the Project Details form.

1) Scheme Type: - This field shows the list of all available project scheme types. Select the required scheme type from the drop down list.

Note: - Whenever a new scheme type is introduced, the details can be added in

the ‘Scheme Type’ under the module “Manage Masters”.

2) Mode of project: - Depending on the scheme type selected, the ‘Mode of Project’ list will be displayed in this drop down field. Select the required Mode of Project.

3) Project Name: - Enter the Project Name.

4) Description: - Provide a brief description about the project in this field.

5) MOFPI Approval Date: - Provide the project approval date by MOFPI official. Pick the date from the pop up calendar.

6) Estimated Start Date: - Select the estimated start date for the project from the calendar.

7) Estimated End Date: - Select the estimated end date for the project.

8) ESCROW A/C no: - Enter the ESCROW account number.

2.)Address details:-

Fields in the Address Details form.

1) State: - Select the state from the drop down box.

2) District: - The Districts in the selected state will be listed. Select the district from the drop down field.

3) City/Village: - The Villages in the selected district will be listed. Select the city or Village from the drop down field.

4) Pin Code: - Enter the valid Pin code of the place.

5) Address: - Enter the Project address.

6) Telephone No with STD code: - Enter the telephone number.

7) Fax No with STD code: - Enter the fax number.

8) Mobile No: - Enter the mobile number.

9) Email: - Enter the valid email id of the applicant.

10) Website: - Enter the Website address.

3.)Agency Details:-

1) Monitoring Agency: - Select the Monitoring agency from the drop down box. The monitoring agency is the company which performs inspection and checking for the project and sends the report to MOFPI.

2) Implementing Agency: - Select the Implementing Agency from the drop down box. The Implementing agency is the company which constructs the project.

3) Total Project Cost (in Rs.):- Enter the Total project cost in rupees.

4) Eligible Project Cost (in Rs.):- Enter the MOFPI approved eligible project cost.

5) MOFPI Assistance (in Rs.): - Enter the Amount sanctioned by MOFPI. The MOFPI assistance amount cannot be greater than the Total Project cost.

After filling all these details in this page, click on proceed.

Optional Project Details

This page contains some optional forms. The optional form details in this page are given as links. Click on any link to find the form and fill it. The links for the forms appearing in this page depends on the scheme type selected at the time of adding the project details.

For example, for the scheme 'Mega Food Park', the Optional project details are as shown in the screen below.

Click on 'Promoter's Background' link.

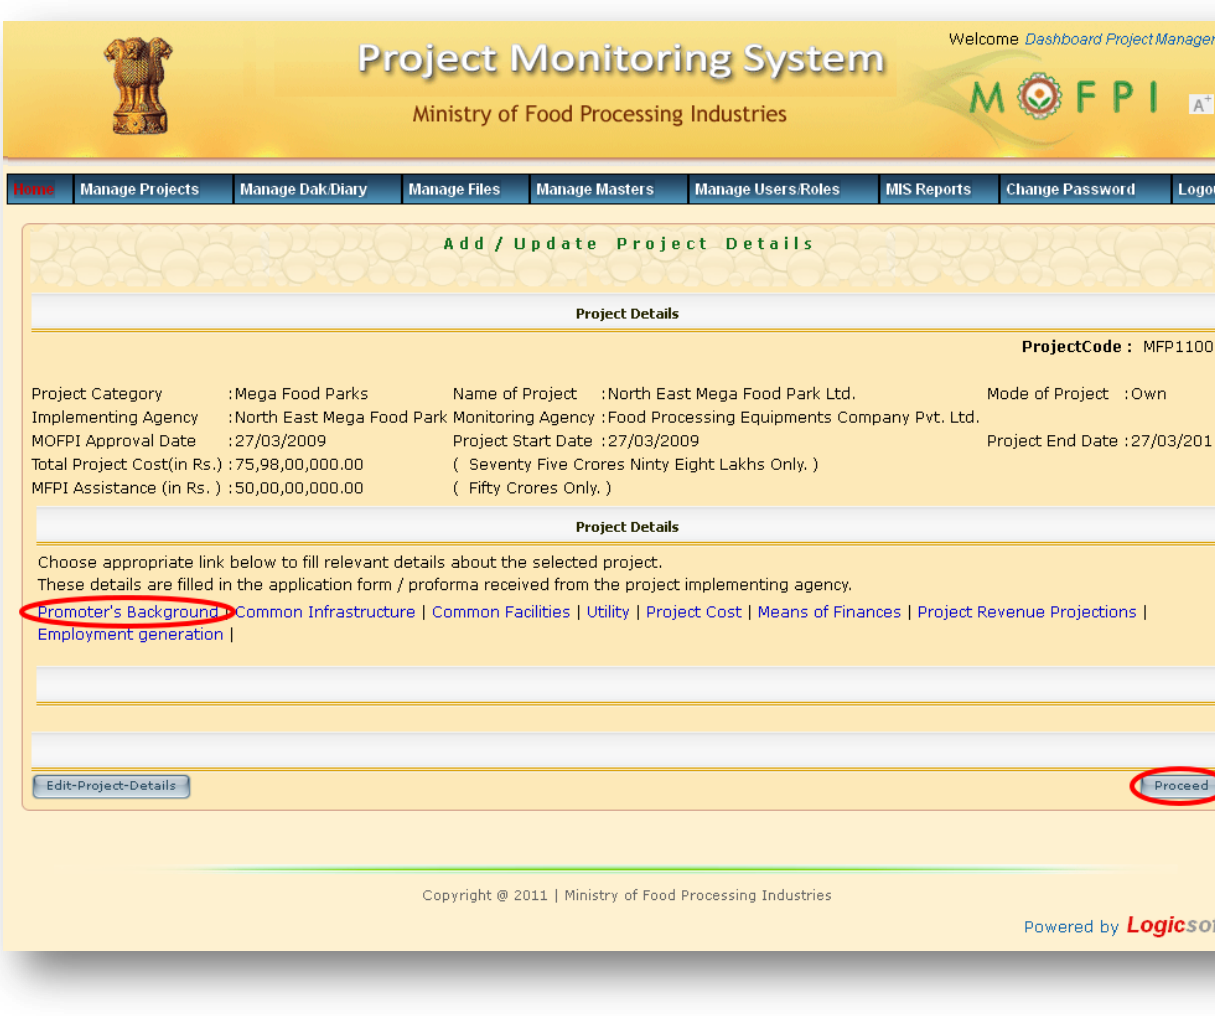
Project Monitoring System
Ministry of Food Processing Industries
Welcome Dashboard Project Manager
MOFPI
Home
Manage Projects
Manage Dak/Diary
Manage Files
Manage Masters
Manage Users/Roles
MIS Reports
Change Password
Add / Update Project Details
Project Details
ProjectCode : MFP1100
Project Category :Mega Food Parks
Name of Project :North East Mega Food Park Ltd.
Mode of Project :Own
Implementing Agency :North East Mega Food Park
Monitoring Agency :Food Processing Equipments Company Pvt. Ltd.
MOFPI Approval Date :27/03/2009
Project Start Date :27/03/2009
Project End Date :27/03/201
Total Project Cost(in Rs.) :75,98,00,000.00
(Seventy Five Crores Ninty Eight Lakhs Only.)
MFPI Assistance (in Rs.) :50,00,00,000.00
(Fifty Crores Only.)
Project Details
Choose appropriate link below to fill relevant details about the selected project.
These details are filled in the application form / proforma received from the project implementing agency.
Promoter's Background | Common Infrastructure | Common Facilities | Utility | Project Cost | Means of Finances | Project Revenue Projections | Employment generation |
Edit-Project-Details
Proceed
Copyright @ 2011 | Ministry of Food Processing Industries
Powered by Logicsoft

Promoter's Background

The promoter's Background form contains the fields like Age, Educational Or Professional Qualification, Present Net Worth (In crores) etc. Fill the description for each field and save it.

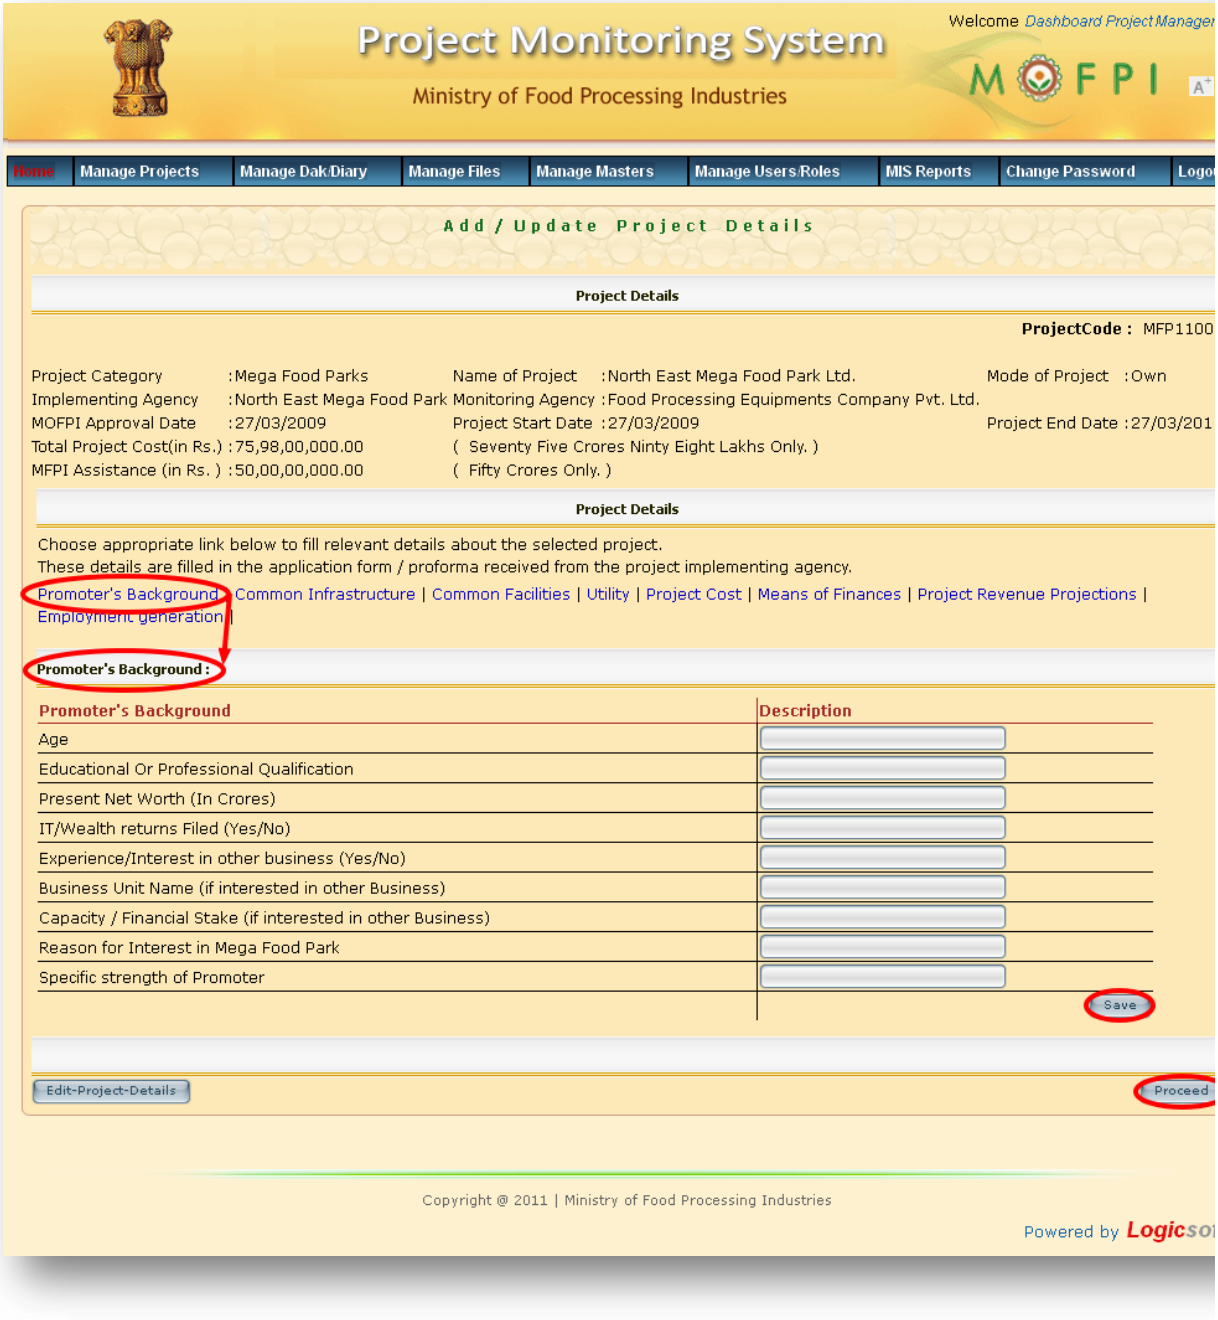
Project Monitoring System
Ministry of Food Processing Industries
Welcome Dashboard Project Manager
MOFPI
Home
Manage Projects
Manage Dak/Diary
Manage Files
Manage Masters
Manage Users/Roles
MIS Reports
Change Password
Add / Update Project Details
Project Details
ProjectCode : MFP1100
Project Category :Mega Food Parks
Name of Project :North East Mega Food Park Ltd.
Mode of Project :Own
Implementing Agency :North East Mega Food Park
Monitoring Agency :Food Processing Equipments Company Pvt. Ltd.
MOFPI Approval Date :27/03/2009
Project Start Date :27/03/2009
Project End Date :27/03/201
Total Project Cost(in Rs.) :75,98,00,000.00
(Seventy Five Crores Ninty Eight Lakhs Only.)
MFPI Assistance (in Rs.) :50,00,00,000.00
(Fifty Crores Only.)
Project Details
Choose appropriate link below to fill relevant details about the selected project.
These details are filled in the application form / proforma received from the project implementing agency.
Promoter's Background | Common Infrastructure | Common Facilities | Utility | Project Cost | Means of Finances | Project Revenue Projections | Employment generation |
Promoter's Background :
Promoter's Background
Description
Age
Educational Or Professional Qualification
Present Net Worth (In Crores)
IT/Wealth returns Filed (Yes/No)
Experience/Interest in other business (Yes/No)
Business Unit Name (if interested in other Business)
Capacity / Financial Stake (if interested in other Business)
Reason for Interest in Mega Food Park
Specific strength of Promoter
Save
Edit-Project-Details
Proceed
Copyright @ 2011 | Ministry of Food Processing Industries
Powered by Logicsoft

Click on ‘Proceed’ to find the next page.

Milestone(s) of your project:-

The major activities in the project are called milestones. For each milestone there could be certain number of related activities (sub activity details).

Filling the milestone details:-

Select the Milestone Name by clicking on the check box of the milestone for which details are to be updated.

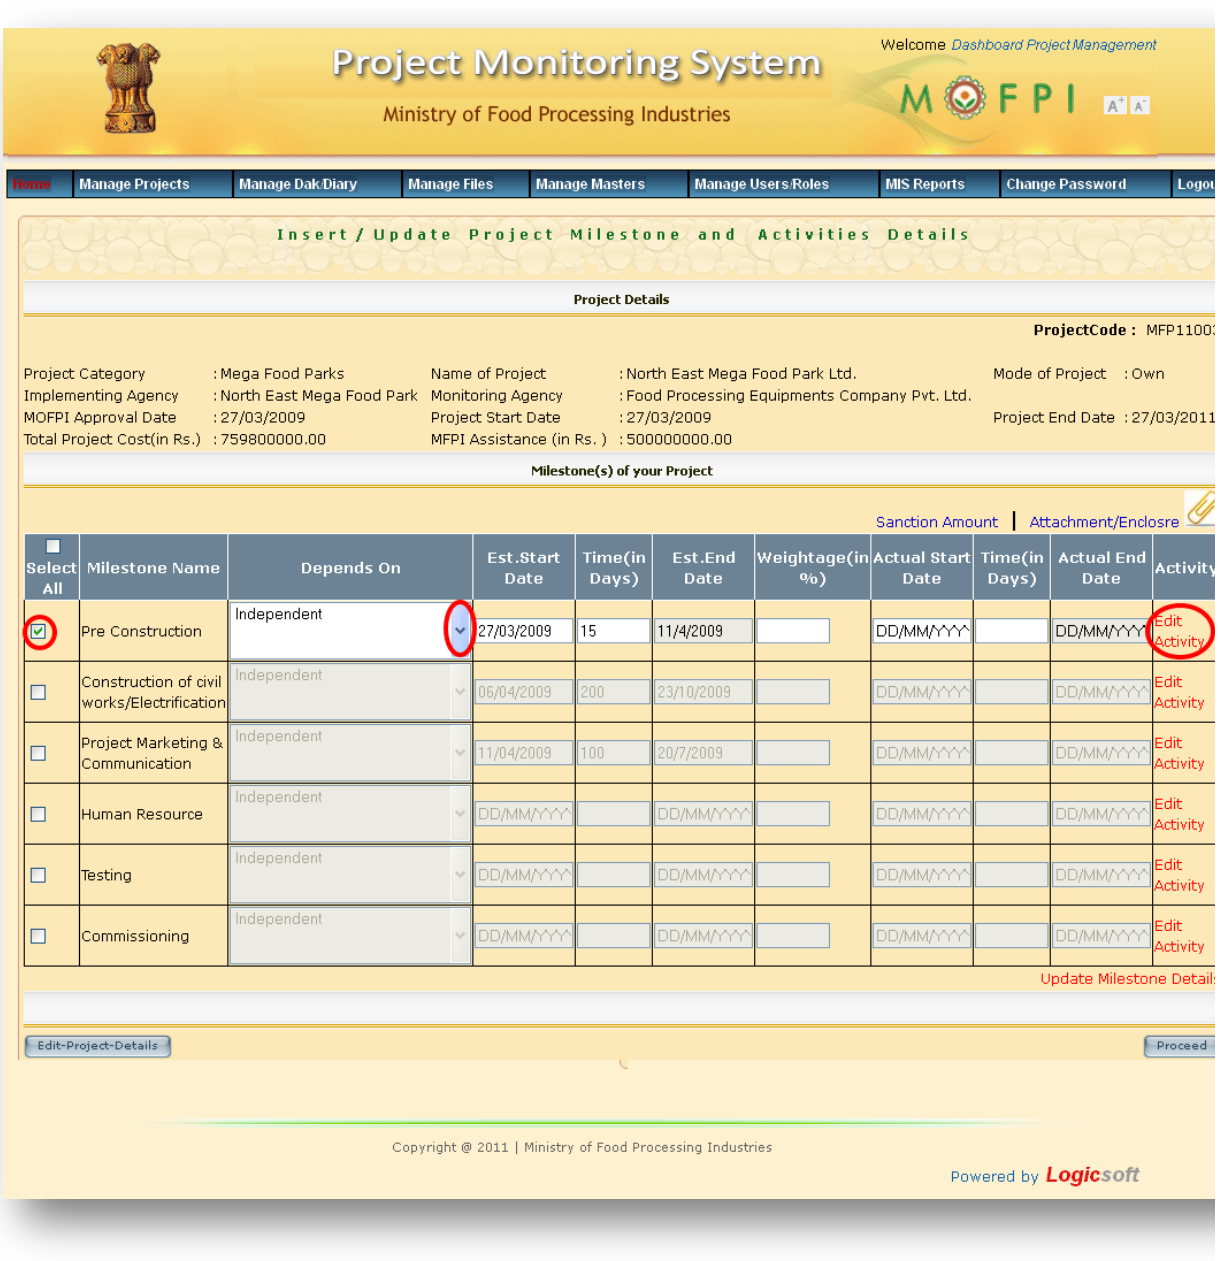

If the milestone depends on any other milestone, then click on the 'Depends On' drop down box and select the required milestone.

Est. Start Date: - select the estimated start date from the calendar.

Time in days: - Enter the time in days to complete the milestone.

Est. End Date: - once the user enters the 'time in days', the system will calculate the estimated end date for that milestone (User need not calculate the end date

and enter it).

Weightage: - Enter the Weightage in percentage.

Actual Start Date: - Enter the Actual start date of the project from the calendar.

Time in days: - enter the actual time taken for completion of the milestone in days.

Actual End Date: - once the user enters the 'time in days', the system will calculate the Actual end date and will appear in this field.

Fill all the Milestone details.

Click on '**Edit Activity**' to find the activities for the selected milestone.

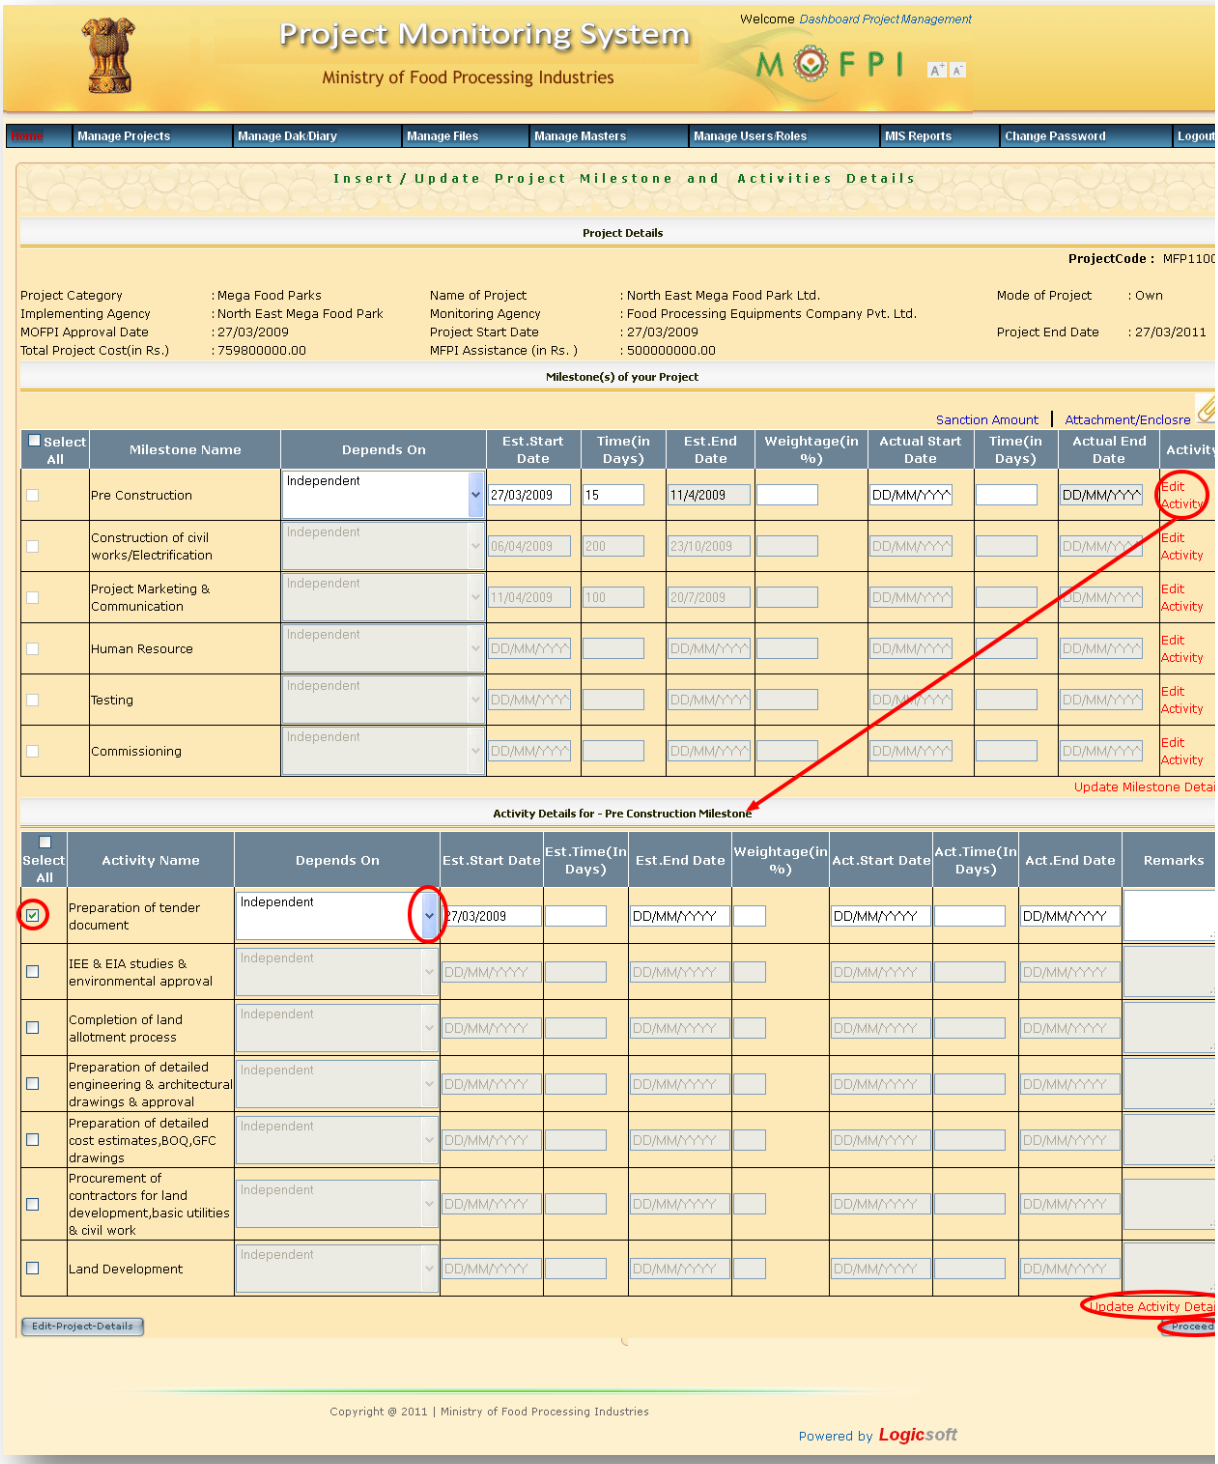
Project Monitoring System
Ministry of Food Processing Industries
Welcome Dashboard Project Management
MOFPI
Home
Manage Projects
Manage Dak/Diary
Manage Files
Manage Masters
Manage Users/Roles
MIS Reports
Change Password
Logout
Insert / Update Project Milestone and Activities Details
Project Details
ProjectCode : MFP1100
Project Category : Mega Food Parks
Implementing Agency : North East Mega Food Park
MOFPI Approval Date : 27/03/2009
Total Project Cost(in Rs.) : 759800000.00
Name of Project : North East Mega Food Park Ltd.
Monitoring Agency : Food Processing Equipments Company Pvt. Ltd.
Project Start Date : 27/03/2009
MFPI Assistance (in Rs.) : 500000000.00
Mode of Project : Own
Project End Date : 27/03/2011
Milestone(s) of your Project
Sanction Amount | Attachment/Enclosre
Select All
Milestone Name
Depends On
Est.Start Date
Time(in Days)
Est.End Date
Weightage(in %)
Actual Start Date
Time(in Days)
Actual End Date
Activity
Pre Construction
Independent
27/03/2009
15
11/4/2009
DD/MM/YYYY
Edit Activity
Construction of civil works/Electrification
06/04/2009
200
23/10/2009
Project Marketing & Communication
11/04/2009
100
20/7/2009
Human Resource
Testing
Commissioning
Update Milestone Detai
Activity Details for - Pre Construction Milestone
Activity Name
Act.Start Date
Act.Time(In Days)
Act.End Date
Remarks
Preparation of tender document
IEE & EIA studies & environmental approval
Completion of land allotment process
Preparation of detailed engineering & architectural drawings & approval
Preparation of detailed cost estimates,BOQ,GFC drawings
Procurement of contractors for land development,basic utilities & civil work
Land Development
Update Activity Detai
Edit-Project-Details
Proceed
Copyright @ 2011 | Ministry of Food Processing Industries
Powered by Logicsoft

Click on ‘Edit Activity’ under Activity column for any Milestone to find the list of activities for the selected milestone. From the list of activities, select any Activity by clicking on the check box of the required activity.

To enter the activity details, select the activity Name.

If the selected activity depends on any other activity, then click on the ‘Depends On’ drop down box and select the required one.

Est. Start Date: - select the estimated start date from the calendar.

Est. Time in days: - Enter the estimated time in days to complete the activity.

Est. End Date: - once the user enters the estimated ‘time in days’, the system will calculate the estimated end date. (User need not calculate this date and enter it).

Weightage: - Enter the Weightage in percentage.

Act. Start Date: - Enter the Actual start date from the calendar.

Act. Time in days: - enter the actual time taken for completion of the activity.

Act. End Date: - once the user enters the ‘time in days’, the system will calculate the Actual end date of the activity.

Sanction Amount

Click on 'Sanction Amount' link in the Milestone details page to find the form where the percentage of sanctioned amount can be mentioned.

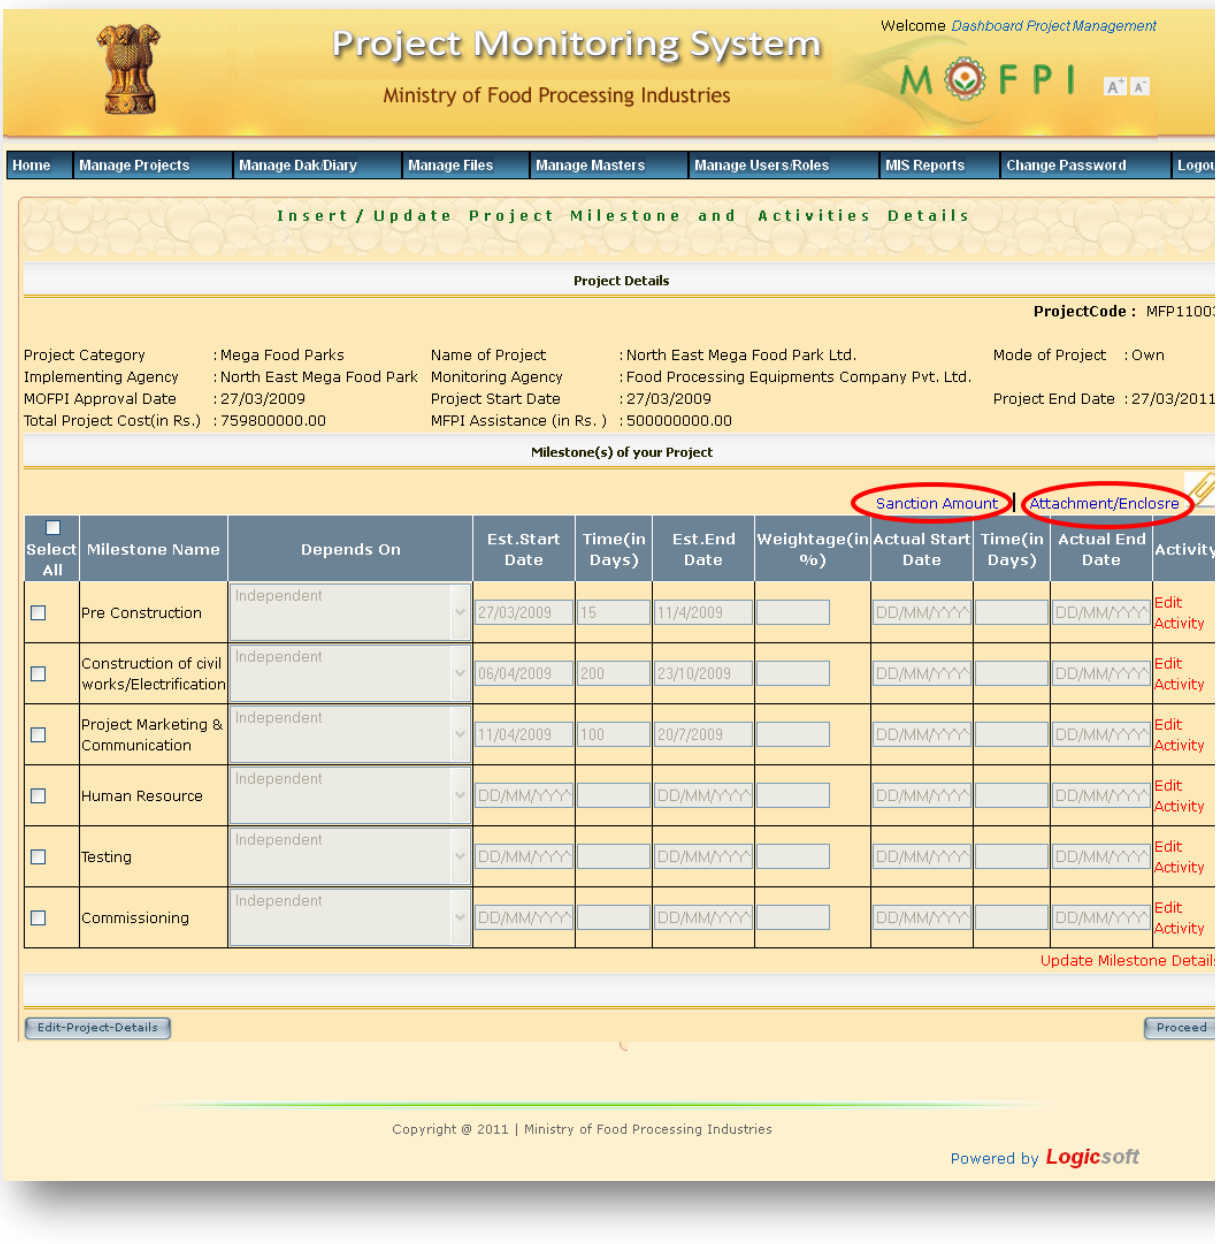

Add New Sanction Amount detail:-

Add New Sanction details according to the requirement. For each sanction amount, enter the percentage (Total percentage of all milestones put together should not exceed 100). Based on the percentage entered, the system will calculate the Amount for that milestone. Enter the sanctioned date, Released date etc.

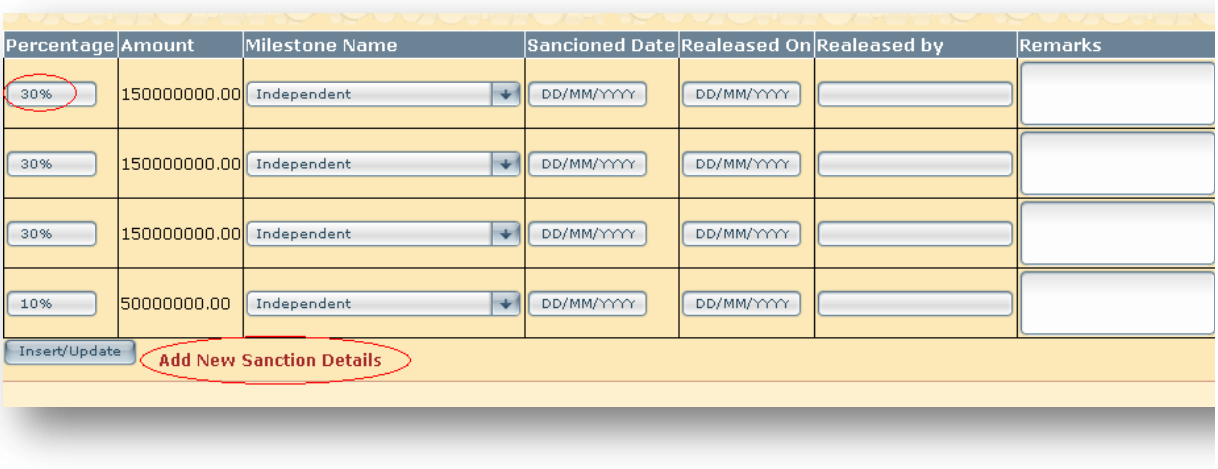

MOFPI will release the sanction amounts on different stages (based on the completion & inspection of activities).

Select the Milestone from the drop down box according to the percentage (Weightage order) allotted and click on 'Insert/Update' to save it.

Attachment/enclosure:-

To attach any file or enclosure, Click on 'Attachment/enclosure'.

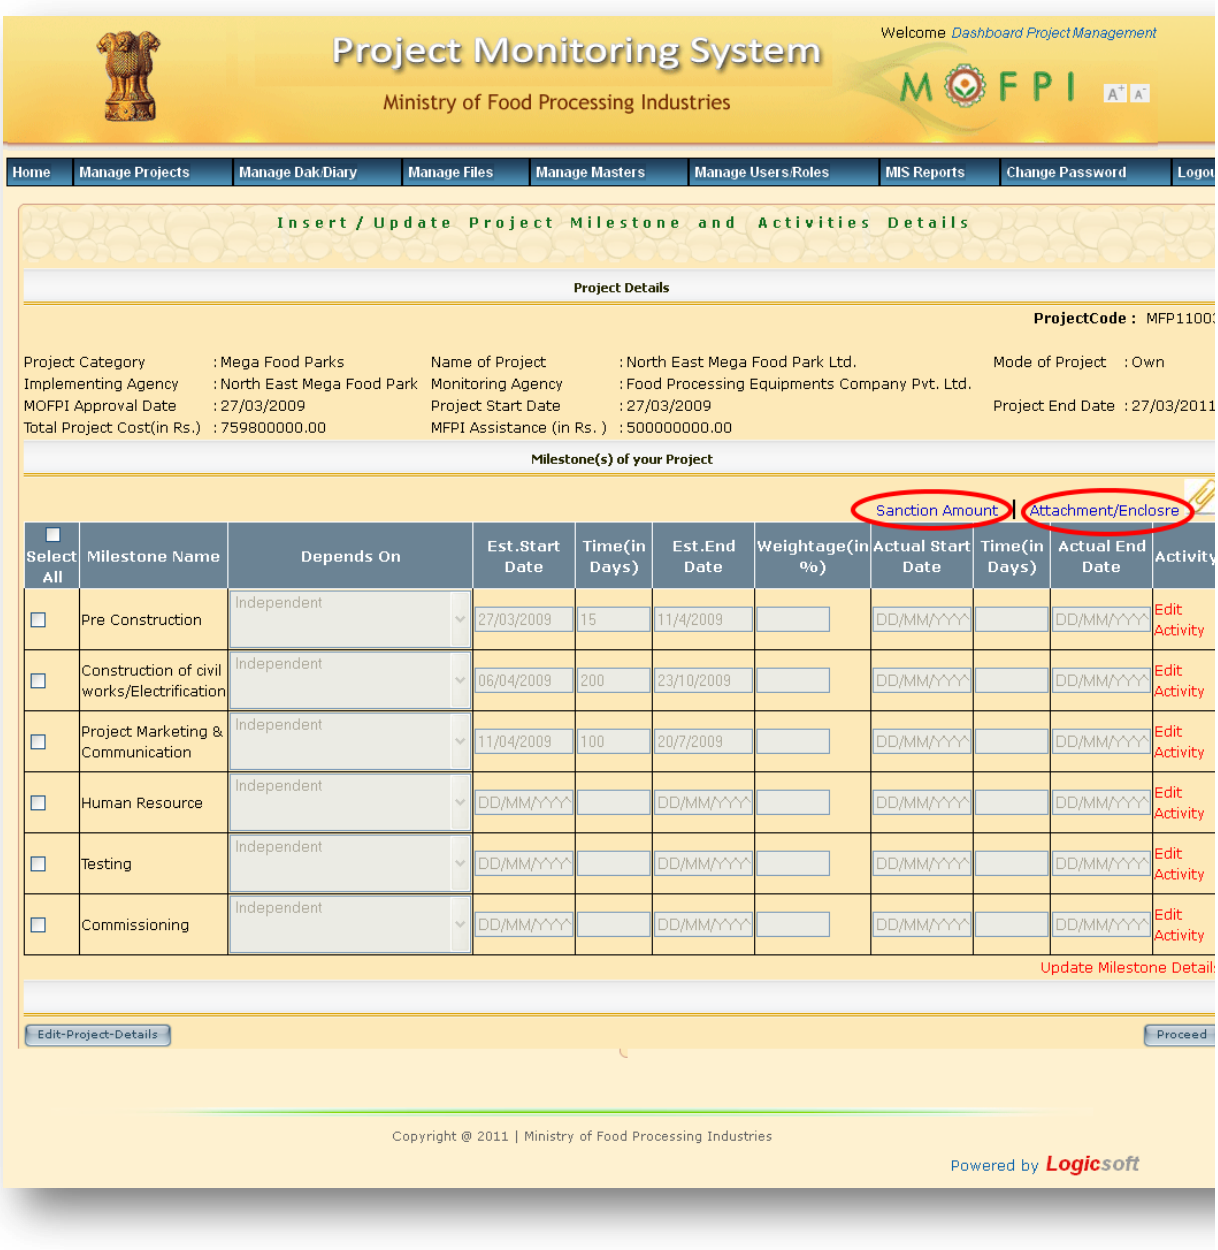

In the window which appears click on Browse and the file upload page will pop-up. Select the file from the local system and click on 'Open'.

The path of the file uploaded can be seen in the 'file name' field.

Enter the title of the file and remarks. Click on ‘attach’ to upload the file.

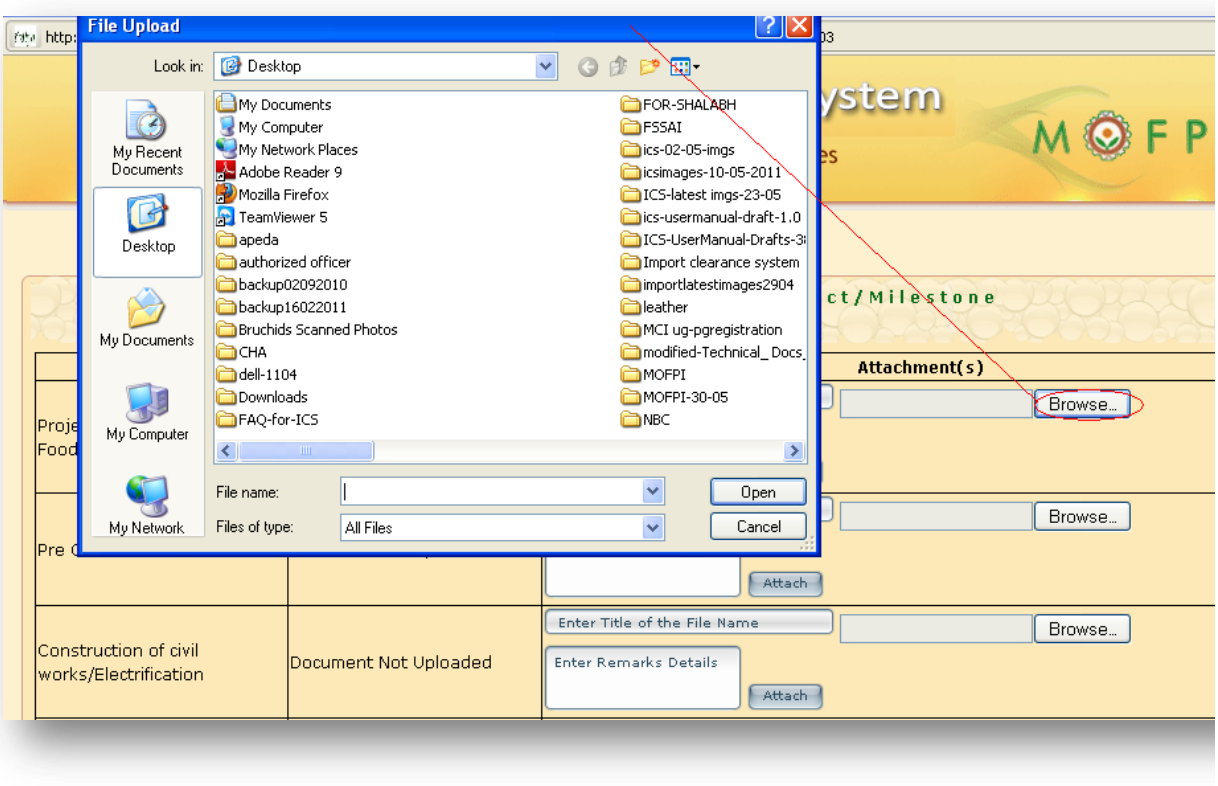

After filling all the details click on proceed to find the project summary detail.

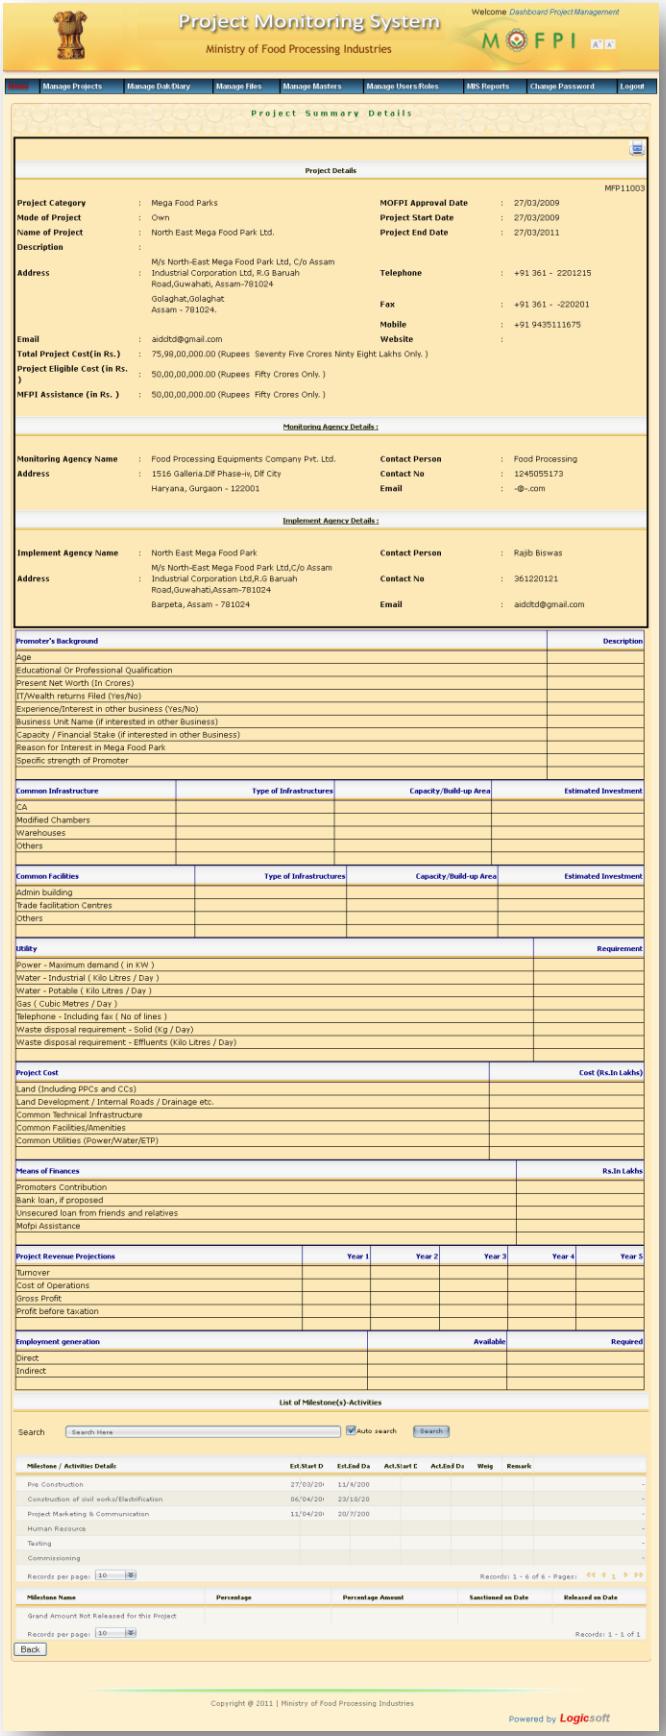
Project Monitoring System
Ministry of Food Processing Industries
Welcome Dashboard Project Management
MOFPI
Manage Projects
Manage Dak Diary
Manage Files
Manage Masters
Manage Users Roles
MIS Reports
Change Password
Logout
Project Summary Details
Project Details
MFP11003
Project Category : Mega Food Parks
Mode of Project : Own
Name of Project : North East Mega Food Park Ltd.
Description :
Address : M/s North-East Mega Food Park Ltd, C/o Assam Industrial Corporation Ltd, R.G Baruah Road,Guwahati, Assam-781024
Golaghat,Golaghat Assam - 781024.
Email : aidcltd@gmail.com
Total Project Cost(in Rs.) : 75,98,00,000.00 (Rupees Seventy Five Crores Ninty Eight Lakhs Only.)
Project Eligible Cost (in Rs.) : 50,00,00,000.00 (Rupees Fifty Crores Only.)
MFPI Assistance (in Rs.) : 50,00,00,000.00 (Rupees Fifty Crores Only.)
MOFPI Approval Date : 27/03/2009
Project Start Date : 27/03/2009
Project End Date : 27/03/2011
Telephone : +91 361 - 2201215
Fax : +91 361 - -220201
Mobile : +91 9435111675
Website :
Monitoring Agency Details :
Monitoring Agency Name : Food Processing Equipments Company Pvt. Ltd.
Address : 1516 Galleria.Dlf Phase-iv, Dlf City Haryana, Gurgaon - 122001
Contact Person : Food Processing
Contact No : 1245055173
Email : -@-.com
Implement Agency Details :
Implement Agency Name : North East Mega Food Park
Address : M/s North-East Mega Food Park Ltd,C/o Assam Industrial Corporation Ltd,R.G Baruah Road,Guwahati,Assam-781024 Barpeta, Assam - 781024
Contact Person : Rajib Biswas
Contact No : 361220121
Email : aidcltd@gmail.com
Promoter's Background
Description
Age
Educational Or Professional Qualification
Present Net Worth (In Crores)
IT/Wealth returns Filed (Yes/No)
Experience/Interest in other business (Yes/No)
Business Unit Name (if interested in other Business)
Capacity / Financial Stake (if interested in other Business)
Reason for Interest in Mega Food Park
Specific strength of Promoter
Common Infrastructure
Type of Infrastructures
Capacity/Build-up Area
Estimated Investment
CA
Modified Chambers
Warehouses
Others
Common Facilities
Type of Infrastructures
Capacity/Build-up Area
Estimated Investment
Admin building
Trade facilitation Centres
Others
Utility
Requirement
Power - Maximum demand (in KW)
Water - Industrial (Kilo Litres / Day)
Water - Potable (Kilo Litres / Day)
Gas (Cubic Metres / Day)
Telephone - Including fax (No of lines)
Waste disposal requirement - Solid (Kg / Day)
Waste disposal requirement - Effluents (Kilo Litres / Day)
Project Cost
Cost (Rs.In Lakhs)
Land (Including PPCs and CCs)
Land Development / Internal Roads / Drainage etc.
Common Technical Infrastructure
Common Facilities/Amenities
Common Utilities (Power/Water/ETP)
Means of Finances
Rs.In Lakhs
Promoters Contribution
Bank loan, if proposed
Unsecured loan from friends and relatives
Mofpi Assistance
Project Revenue Projections
Year 1
Year 2
Year 3
Year 4
Year 5
Turnover
Cost of Operations
Gross Profit
Profit before taxation
Employment generation
Available
Required
Direct
Indirect
List of Milestone(s)-Activities
Search
Search Here
Auto search
Search
Milestone / Activities Details
Est.Start D
Est.End Da
Act.Start D
Act.End Da
Weig
Remark
Pre Construction
Construction of civil works/Electrification
Project Marketing & Communication
Human Resource
Testing
Commissioning
Records per page: 10
Records: 1 - 6 of 6 - Pages:
Milestone Name
Percentage
Percentage Amount
Sanctioned on Date
Released on Date
Grand Amount Not Released for this Project
Records per page: 10
Records: 1 - 1 of 1
Back
Copyright @ 2011 | Ministry of Food Processing Industries
Powered by Logicsoft

Update Project Detail

To modify and update any project detail, Move the mouse over 'Manage Projects' and click on 'Projects'.

From the list of projects, find the project to be modified and click on the edit symbol to modify that project's details.

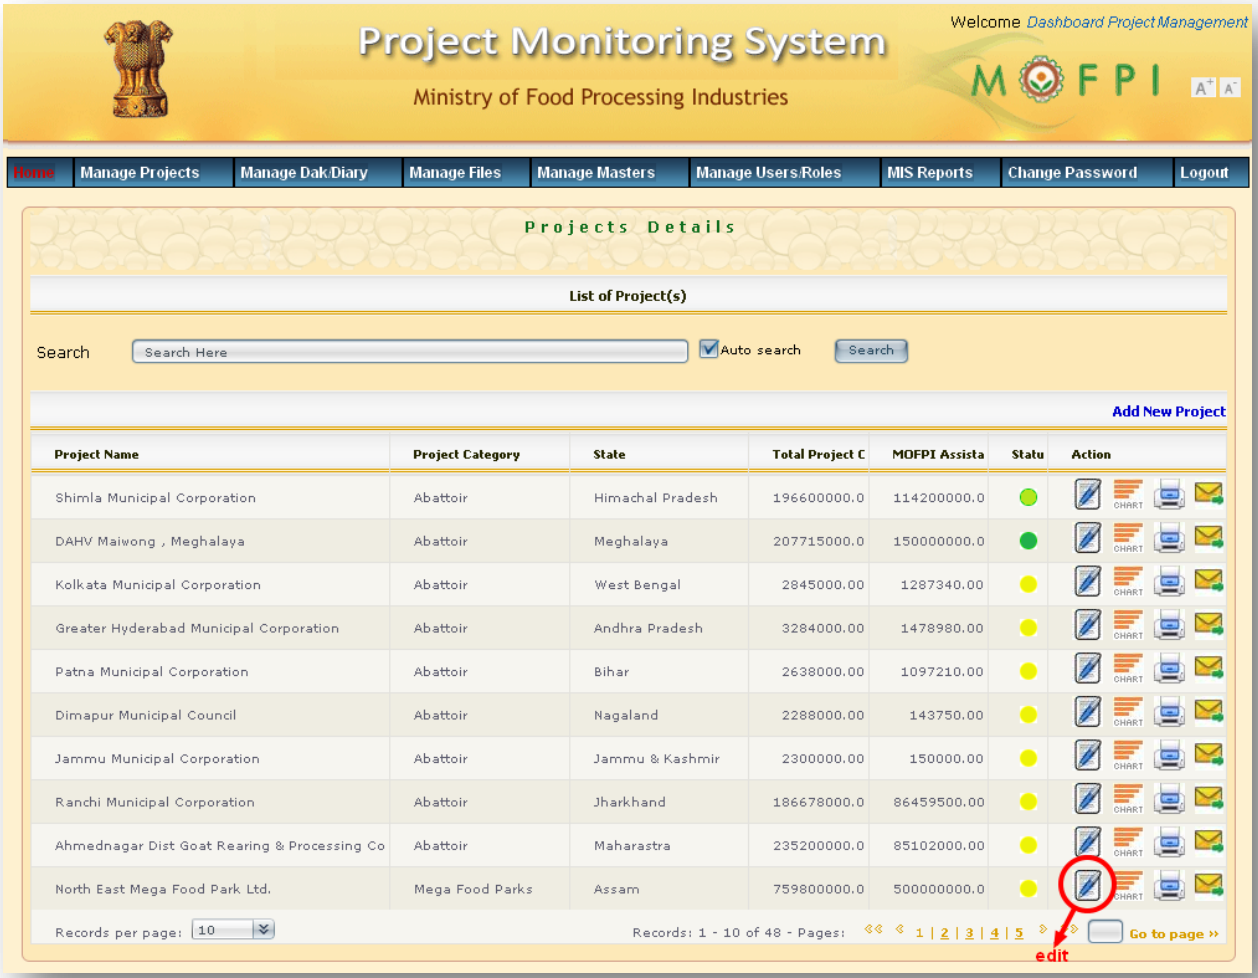
Project Monitoring System
Ministry of Food Processing Industries
Welcome Dashboard Project Management
MOFPI
Home
Manage Projects
Manage Dak/Diary
Manage Files
Manage Masters
Manage Users/Roles
MIS Reports
Change Password
Logout
Projects Details
List of Project(s)
Search
Search Here
Auto search
Search
Add New Project
Project Name
Project Category
State
Total Project C
MOFPI Assista
Statu
Action
Shimla Municipal Corporation Abattoir Himachal Pradesh 196600000.0 114200000.0
DAHV Maiwong , Meghalaya Abattoir Meghalaya 207715000.0 150000000.0
Kolkata Municipal Corporation Abattoir West Bengal 2845000.00 1287340.00
Greater Hyderabad Municipal Corporation Abattoir Andhra Pradesh 3284000.00 1478980.00
Patna Municipal Corporation Abattoir Bihar 2638000.00 1097210.00
Dimapur Municipal Council Abattoir Nagaland 2288000.00 143750.00
Jammu Municipal Corporation Abattoir Jammu & Kashmir 2300000.00 150000.00
Ranchi Municipal Corporation Abattoir Jharkhand 186678000.0 86459500.00
Ahmednagar Dist Goat Rearing & Processing Co Abattoir Maharastra 235200000.0 85102000.00
North East Mega Food Park Ltd. Mega Food Parks Assam 759800000.0 500000000.0
Records per page: 10
Records: 1 - 10 of 48 - Pages: 1 | 2 | 3 | 4 | 5
Go to page »
edit

As shown in the screen below, the project details (first form details) will be displayed. Modify the required fields and proceed to the next page.

Note:- The Scheme Type cannot be modified.

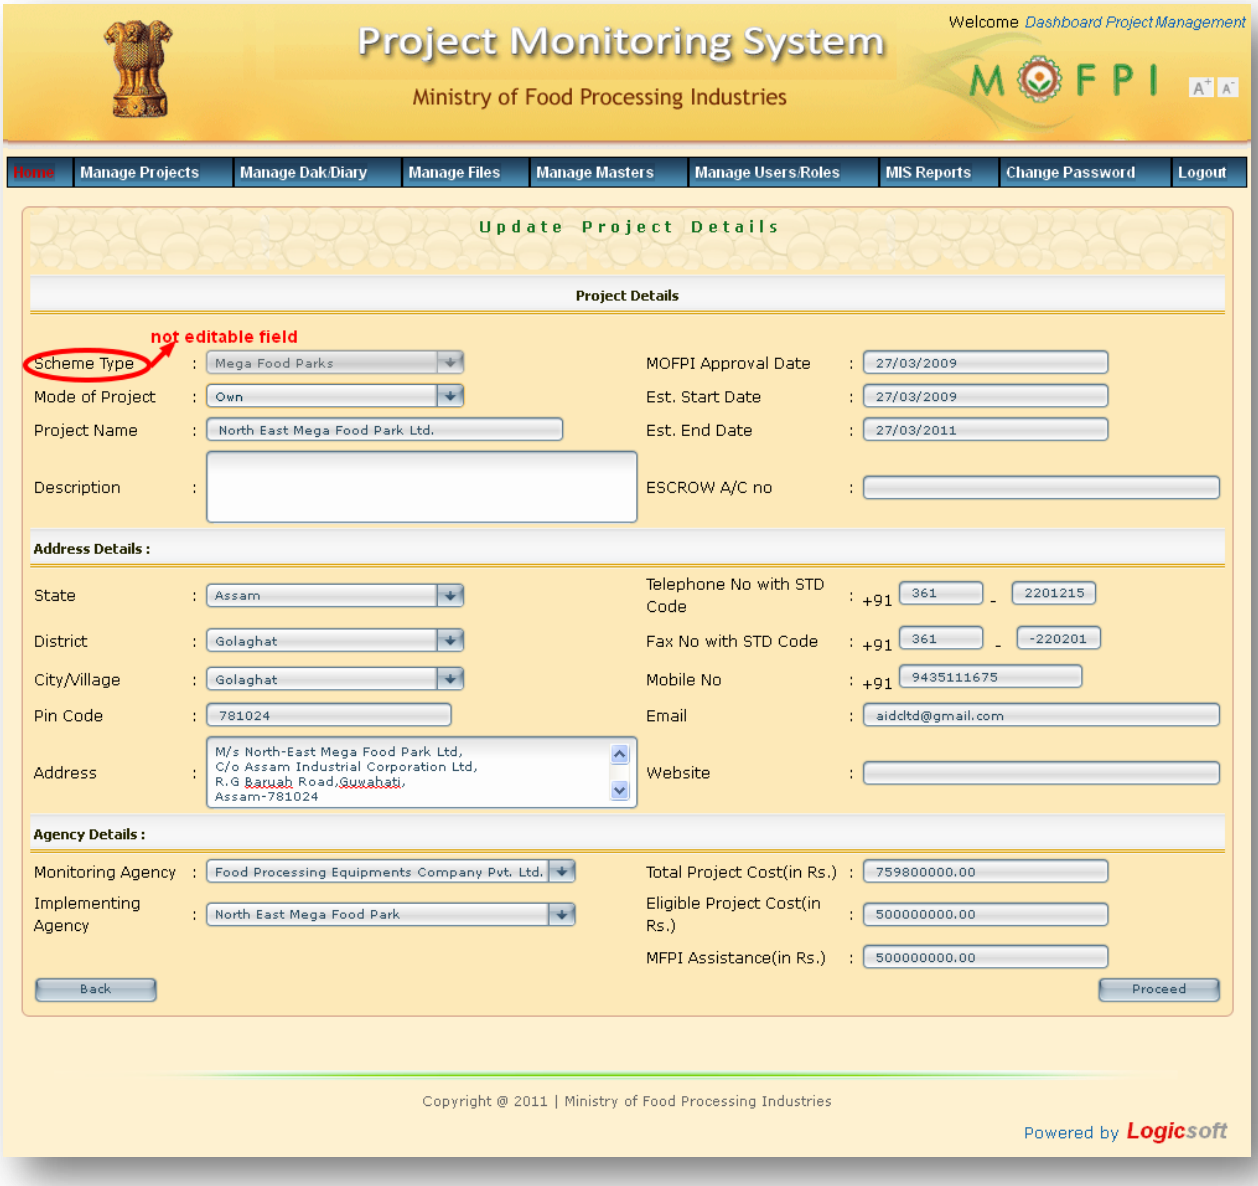
Project Monitoring System
Ministry of Food Processing Industries
Welcome Dashboard Project Management
MOFPI
Home
Manage Projects
Manage Dak/Diary
Manage Files
Manage Masters
Manage Users/Roles
MIS Reports
Change Password
Logout
Update Project Details
Project Details
not editable field
Scheme Type : Mega Food Parks
Mode of Project : Own
Project Name : North East Mega Food Park Ltd.
Description :
MOFPI Approval Date : 27/03/2009
Est. Start Date : 27/03/2009
Est. End Date : 27/03/2011
ESCROW A/C no :
Address Details :
State : Assam
District : Golaghat
City/Village : Golaghat
Pin Code : 781024
Address : M/s North-East Mega Food Park Ltd, C/o Assam Industrial Corporation Ltd, R.G Baruah Road,Guwahati, Assam-781024
Telephone No with STD Code : +91 361 - 2201215
Fax No with STD Code : +91 361 - -220201
Mobile No : +91 9435111675
Email : aidcltd@gmail.com
Website :
Agency Details :
Monitoring Agency : Food Processing Equipments Company Pvt. Ltd.
Implementing Agency : North East Mega Food Park
Total Project Cost(in Rs.) : 759800000.00
Eligible Project Cost(in Rs.) : 500000000.00
MFPI Assistance(in Rs.) : 500000000.00
Back
Proceed
Copyright @ 2011 | Ministry of Food Processing Industries
Powered by Logicsoft

Click on proceed to find the next page.

Click on any link in this page to find the details to be updated. Modify the details and save it.

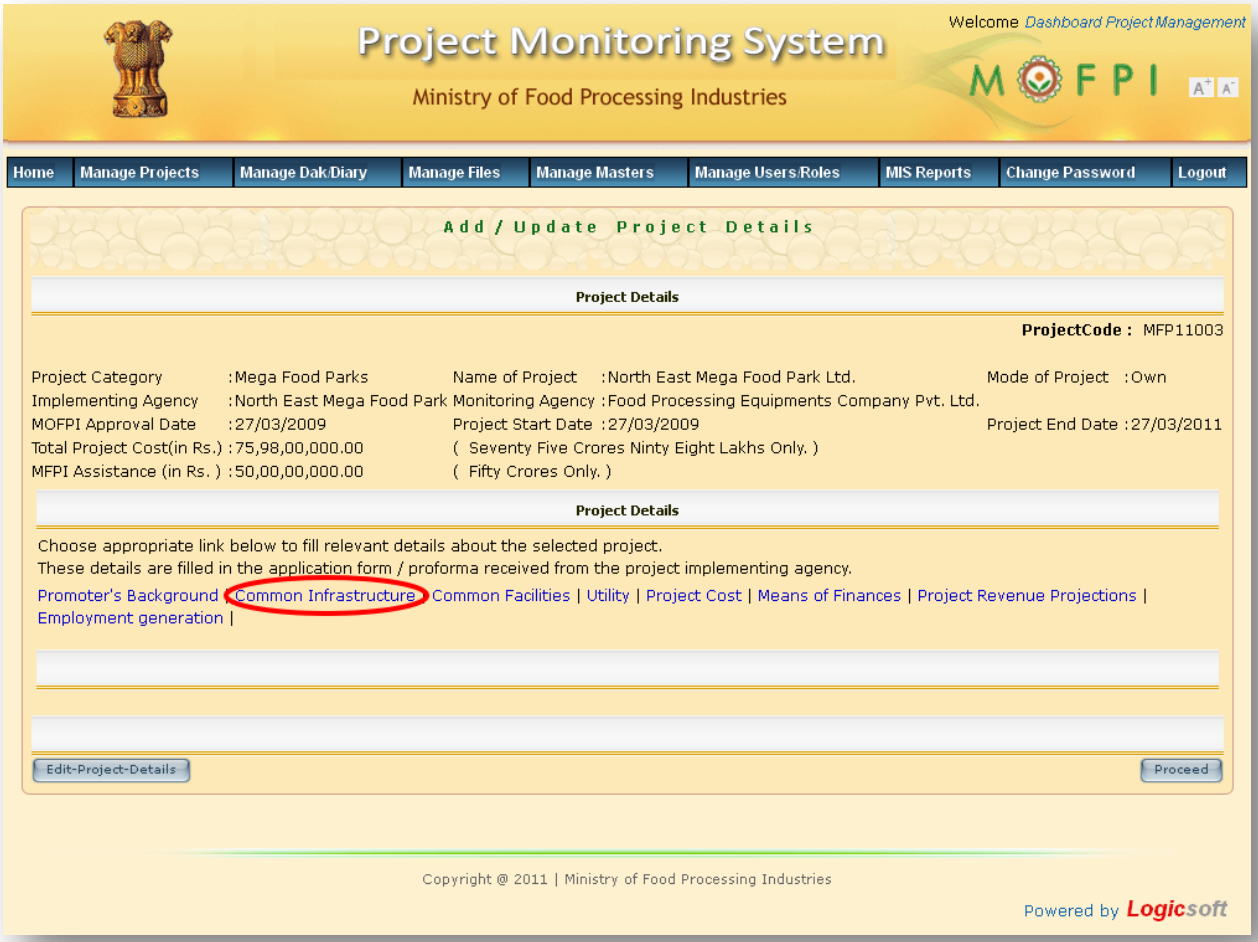
Project Monitoring System
Ministry of Food Processing Industries
Welcome Dashboard Project Management
MOFPI
Home
Manage Projects
Manage Dak/Diary
Manage Files
Manage Masters
Manage Users/Roles
MIS Reports
Change Password
Logout
Add / Update Project Details
Project Details
ProjectCode : MFP11003
Project Category :Mega Food Parks
Name of Project :North East Mega Food Park Ltd.
Mode of Project :Own
Implementing Agency :North East Mega Food Park
Monitoring Agency :Food Processing Equipments Company Pvt. Ltd.
MOFPI Approval Date :27/03/2009
Project Start Date :27/03/2009
Project End Date :27/03/2011
Total Project Cost(in Rs.) :75,98,00,000.00
(Seventy Five Crores Ninty Eight Lakhs Only.)
MFPI Assistance (in Rs.) :50,00,00,000.00
(Fifty Crores Only.)
Project Details
Choose appropriate link below to fill relevant details about the selected project.
These details are filled in the application form / proforma received from the project implementing agency.
Promoter's Background | Common Infrastructure | Common Facilities | Utility | Project Cost | Means of Finances | Project Revenue Projections | Employment generation |
Edit-Project-Details
Proceed
Copyright @ 2011 | Ministry of Food Processing Industries
Powered by Logicsoft

Click on ‘Proceed’ to find the next page.

In the Milestone details page, modify the required fields.

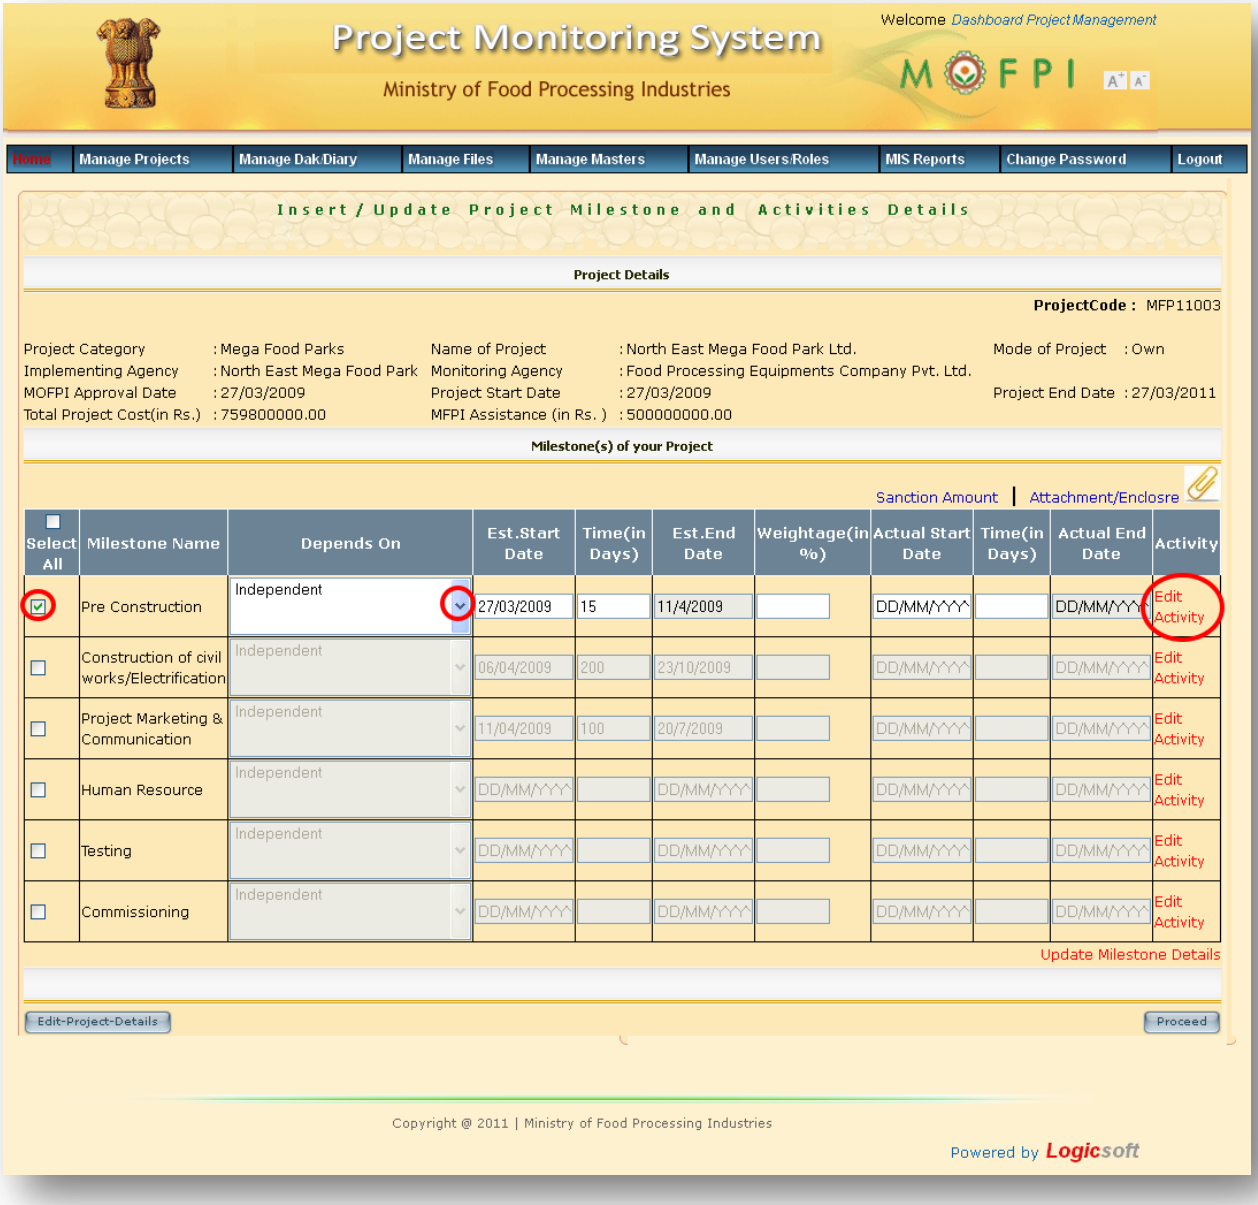

Click on ‘Proceed’ to find the detailed summary of the modified project.

PERT Chart

A PERT chart is a project management tool used to schedule, organize, and coordinate tasks within a project. PERT stands for Program Evaluation Review Technique.

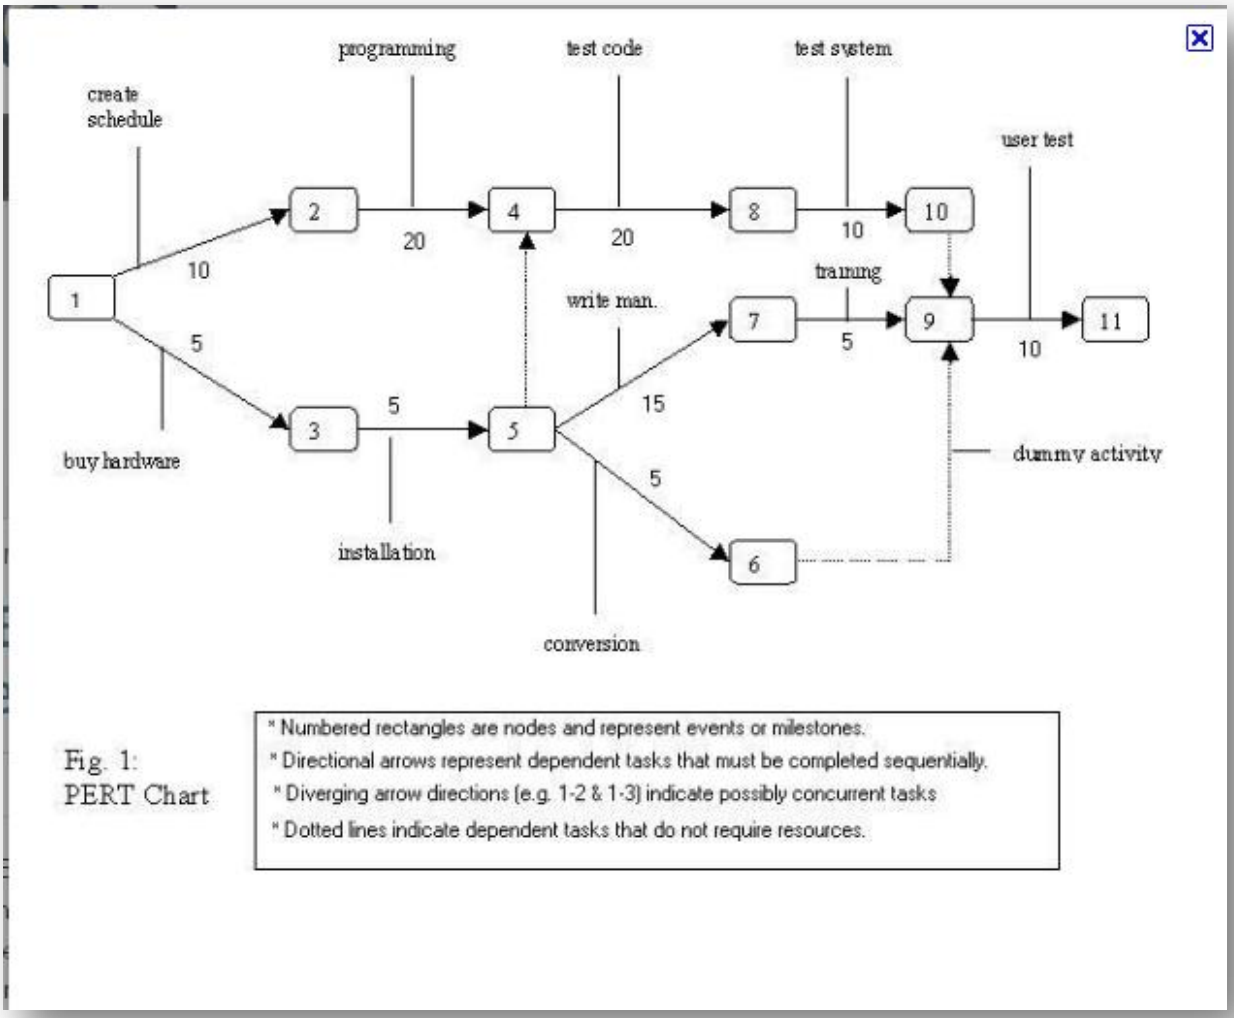

Fig. 1: PERT Chart

A PERT chart presents a graphic illustration of a project as a network diagram consisting of numbered *nodes* (either circles or rectangles) representing events (activities), or milestones in the project linked by labeled *vectors* (directional lines) representing tasks in the project. The direction of the arrows on the lines indicates the sequence of tasks. In the diagram, for example, the tasks between nodes 1, 2, 4, 8, and 10 must be completed in sequence. These are called *dependent* or *serial* tasks. The tasks between nodes 1 and 2 and nodes 1 and 3 are not dependent on the completion of one to start the other and can be undertaken simultaneously.

These tasks are called *parallel* or *concurrent* tasks. Tasks that must be completed in sequence but that don't require resources or completion time are considered to have *event dependency*. These are represented by dotted lines with arrows and are called *dummy activities*. For example, the dashed arrow linking nodes 6 and 9 indicates that the system files must be converted before the user test can take place, but that the resources and time required to prepare for the user test (writing the user manual and user training) are on another path. Numbers on the opposite sides of the vectors indicate the time allotted for the task.

PERT Chart for MOFPI projects

To find the PERT chart for any particular project in the system, Move the mouse over 'Manage Projects' and click on 'Projects'.

From the list of projects find the project for which PERT Chart is to be found.

Project Monitoring System
Ministry of Food Processing Industries
Welcome Dashboard Project Management
MOFPI
Home
Manage Projects
Manage Dak/Diary
Manage Files
Manage Masters
Manage Users/Roles
MIS Reports
Change Password
Logout
Projects Details
List of Project(s)
Search
Search Here
Auto search
Search
Add New Project
Project Name
Project Category
State
Total Project C
MOFPI Assista
Statu
Action
Shimla Municipal Corporation Abattoir Himachal Pradesh 196600000.0 114200000.0
DAHV Maiwong , Meghalaya Abattoir Meghalaya 207715000.0 150000000.0
Kolkata Municipal Corporation Abattoir West Bengal 2845000.00 1287340.00
Greater Hyderabad Municipal Corporation Abattoir Andhra Pradesh 3284000.00 1478980.00
Patna Municipal Corporation Abattoir Bihar 2638000.00 1097210.00
Dimapur Municipal Council Abattoir Nagaland 2288000.00 143750.00
Jammu Municipal Corporation Abattoir Jammu & Kashmir 2300000.00 150000.00
Ranchi Municipal Corporation Abattoir Jharkhand 186678000.0 86459500.00
Ahmednagar Dist Goat Rearing & Processing Co Abattoir Maharastra 235200000.0 85102000.00
North East Mega Food Park Ltd. Mega Food Parks Assam 759800000.0 500000000.0
Records per page: 10
Records: 1 - 10 of 48 - Pages: 1 | 2 | 3 | 4 | 5
Go to page
Copyright @ 2011 | Ministry of Food Processing Industries
Powered by Logicsoft

There are three types of PERT Charts available for each project.

1.) **Estimated Pert Chart**

2.) **Actual Pert Chart**

3.) **Comparison Est/Act**

Choose the Pert Chart type.

Estimated Pert Chart

This chart shows the pictorial representation of the estimated start date and estimated end date for all the Mile stones and related activities in the project.

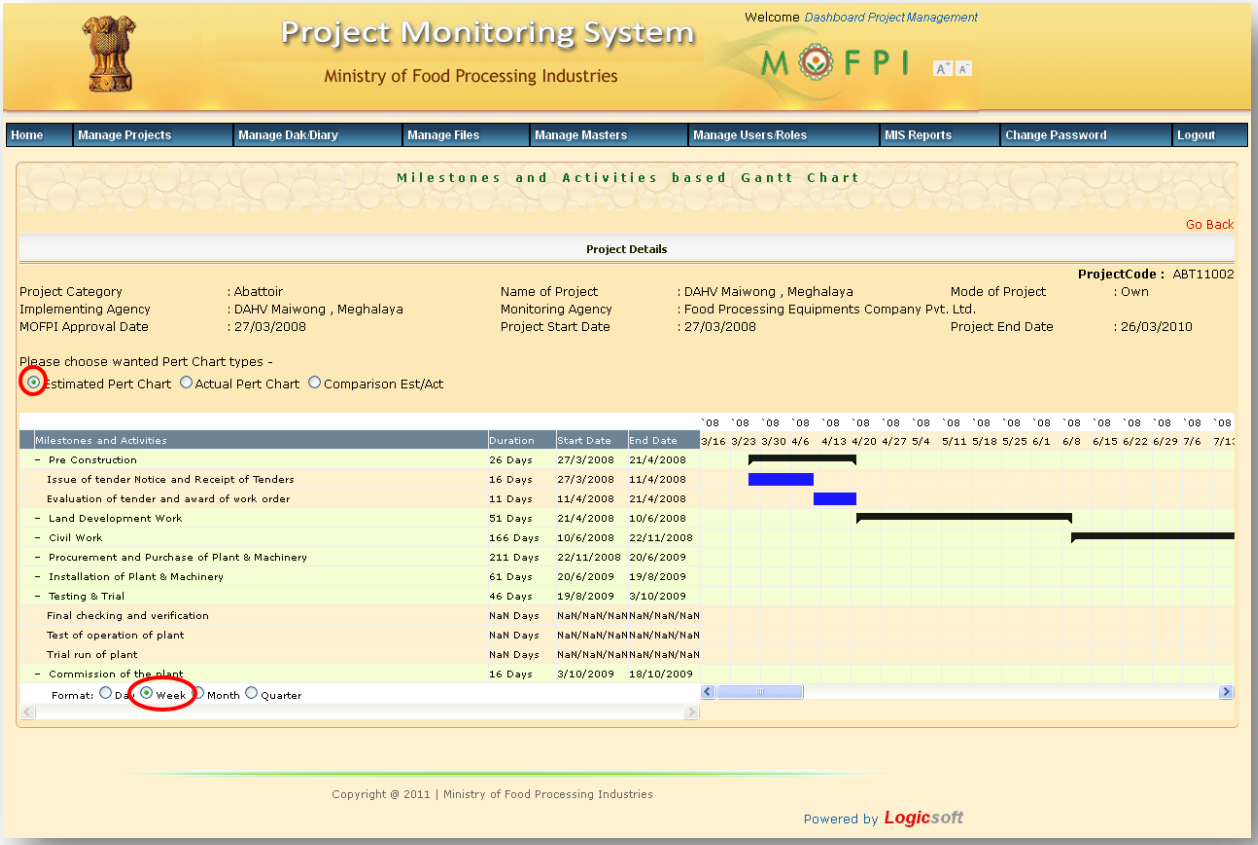
Project Monitoring System
Ministry of Food Processing Industries
Welcome Dashboard Project Management
MOFPI
Home
Manage Projects
Manage Dak/Diary
Manage Files
Manage Masters
Manage Users/Roles
MIS Reports
Change Password
Logout
Milestones and Activities based Gantt Chart
Go Back
Project Details
ProjectCode : ABT11002
Project Category : Abattoir
Name of Project : DAHV Maiwong , Meghalaya
Mode of Project : Own
Implementing Agency : DAHV Maiwong , Meghalaya
Monitoring Agency : Food Processing Equipments Company Pvt. Ltd.
MOFPI Approval Date : 27/03/2008
Project Start Date : 27/03/2008
Project End Date : 26/03/2010
Please choose wanted Pert Chart types -
Estimated Pert Chart
Actual Pert Chart
Comparison Est/Act
Milestones and Activities
Duration
Start Date
End Date
Pre Construction 26 Days 27/3/2008 21/4/2008
Issue of tender Notice and Receipt of Tenders 16 Days 27/3/2008 11/4/2008
Evaluation of tender and award of work order 11 Days 11/4/2008 21/4/2008
Land Development Work 51 Days 21/4/2008 10/6/2008
Civil Work 166 Days 10/6/2008 22/11/2008
Procurement and Purchase of Plant & Machinery 211 Days 22/11/2008 20/6/2009
Installation of Plant & Machinery 61 Days 20/6/2009 19/8/2009
Testing & Trial 46 Days 19/8/2009 3/10/2009
Final checking and verification NaN Days NaN/NaN/NaN NaN/NaN/NaN
Test of operation of plant NaN Days NaN/NaN/NaN NaN/NaN/NaN
Trial run of plant NaN Days NaN/NaN/NaN NaN/NaN/NaN
Commission of the plant 16 Days 3/10/2009 18/10/2009
Format: Day Week Month Quarter
Copyright @ 2011 | Ministry of Food Processing Industries
Powered by Logicsoft

User can get an overview of the estimated time duration required to complete each activity under a milestone and also the total time required to complete any milestone as a whole.

Actual Pert Chart

This chart shows the pictorial representation of the actual start date and end date for all the Mile stones and related activities in the project.

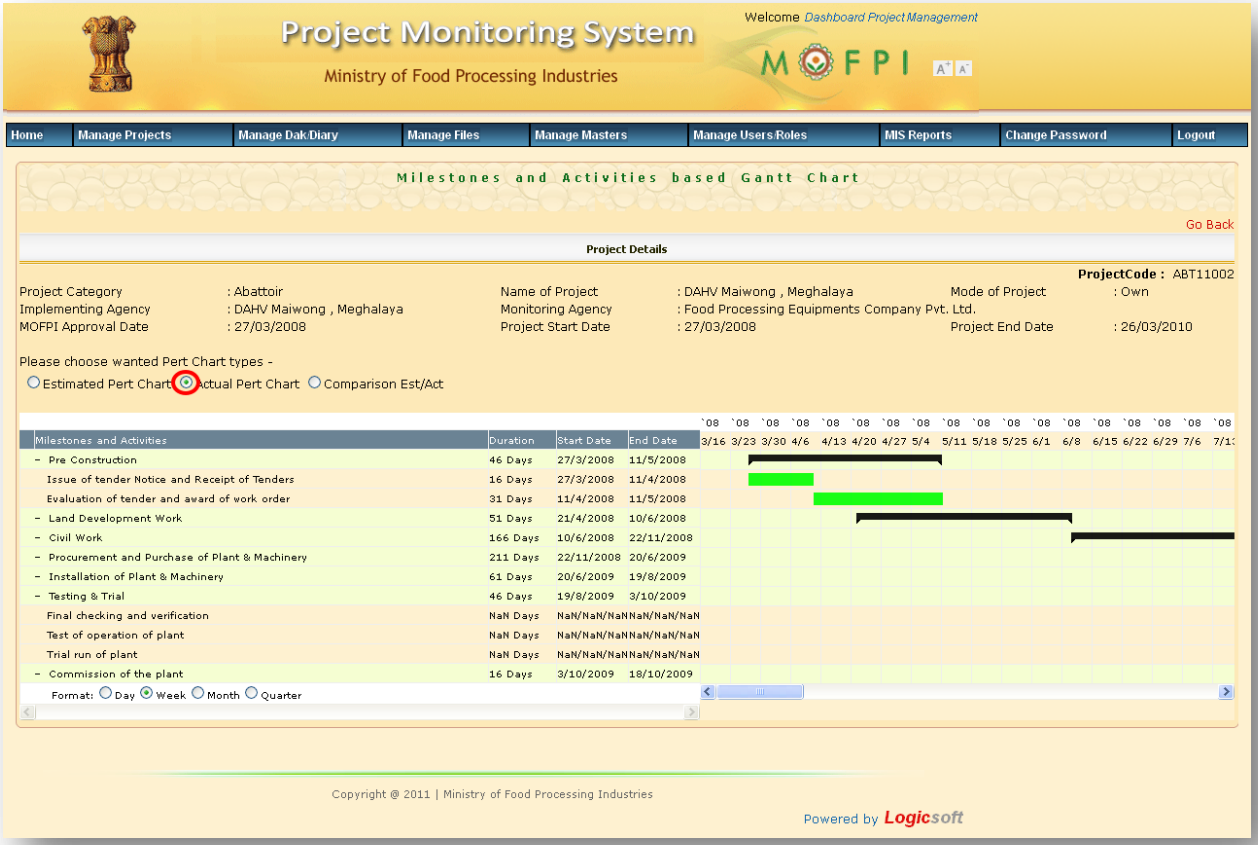
Project Monitoring System
Ministry of Food Processing Industries
Welcome Dashboard Project Management
MOFPI
Home
Manage Projects
Manage Dak/Diary
Manage Files
Manage Masters
Manage Users/Roles
MIS Reports
Change Password
Logout
Milestones and Activities based Gantt Chart
Go Back
Project Details
ProjectCode : ABT11002
Project Category : Abattoir
Name of Project : DAHV Maiwong , Meghalaya
Mode of Project : Own
Implementing Agency : DAHV Maiwong , Meghalaya
Monitoring Agency : Food Processing Equipments Company Pvt. Ltd.
MOFPI Approval Date : 27/03/2008
Project Start Date : 27/03/2008
Project End Date : 26/03/2010
Please choose wanted Pert Chart types -
Estimated Pert Chart
Actual Pert Chart
Comparison Est/Act
Milestones and Activities
Duration
Start Date
End Date
Pre Construction 46 Days 27/3/2008 11/5/2008
Issue of tender Notice and Receipt of Tenders 16 Days 27/3/2008 11/4/2008
Evaluation of tender and award of work order 31 Days 11/4/2008 11/5/2008
Land Development Work 51 Days 21/4/2008 10/6/2008
Civil Work 166 Days 10/6/2008 22/11/2008
Procurement and Purchase of Plant & Machinery 211 Days 22/11/2008 20/6/2009
Installation of Plant & Machinery 61 Days 20/6/2009 19/8/2009
Testing & Trial 46 Days 19/8/2009 3/10/2009
Final checking and verification NaN Days NaN/NaN/NaN NaN/NaN/NaN
Test of operation of plant NaN Days NaN/NaN/NaN NaN/NaN/NaN
Trial run of plant NaN Days NaN/NaN/NaN NaN/NaN/NaN
Commission of the plant 16 Days 3/10/2009 18/10/2009
Format: Day Week Month Quarter
Copyright @ 2011 | Ministry of Food Processing Industries
Powered by Logicsoft

The actual time taken for the completion of each activity under a milestone will be shown in this chart.

Comparison Est/Act

A graphical comparison of the estimated pert chat and actual pert chart can be found here.

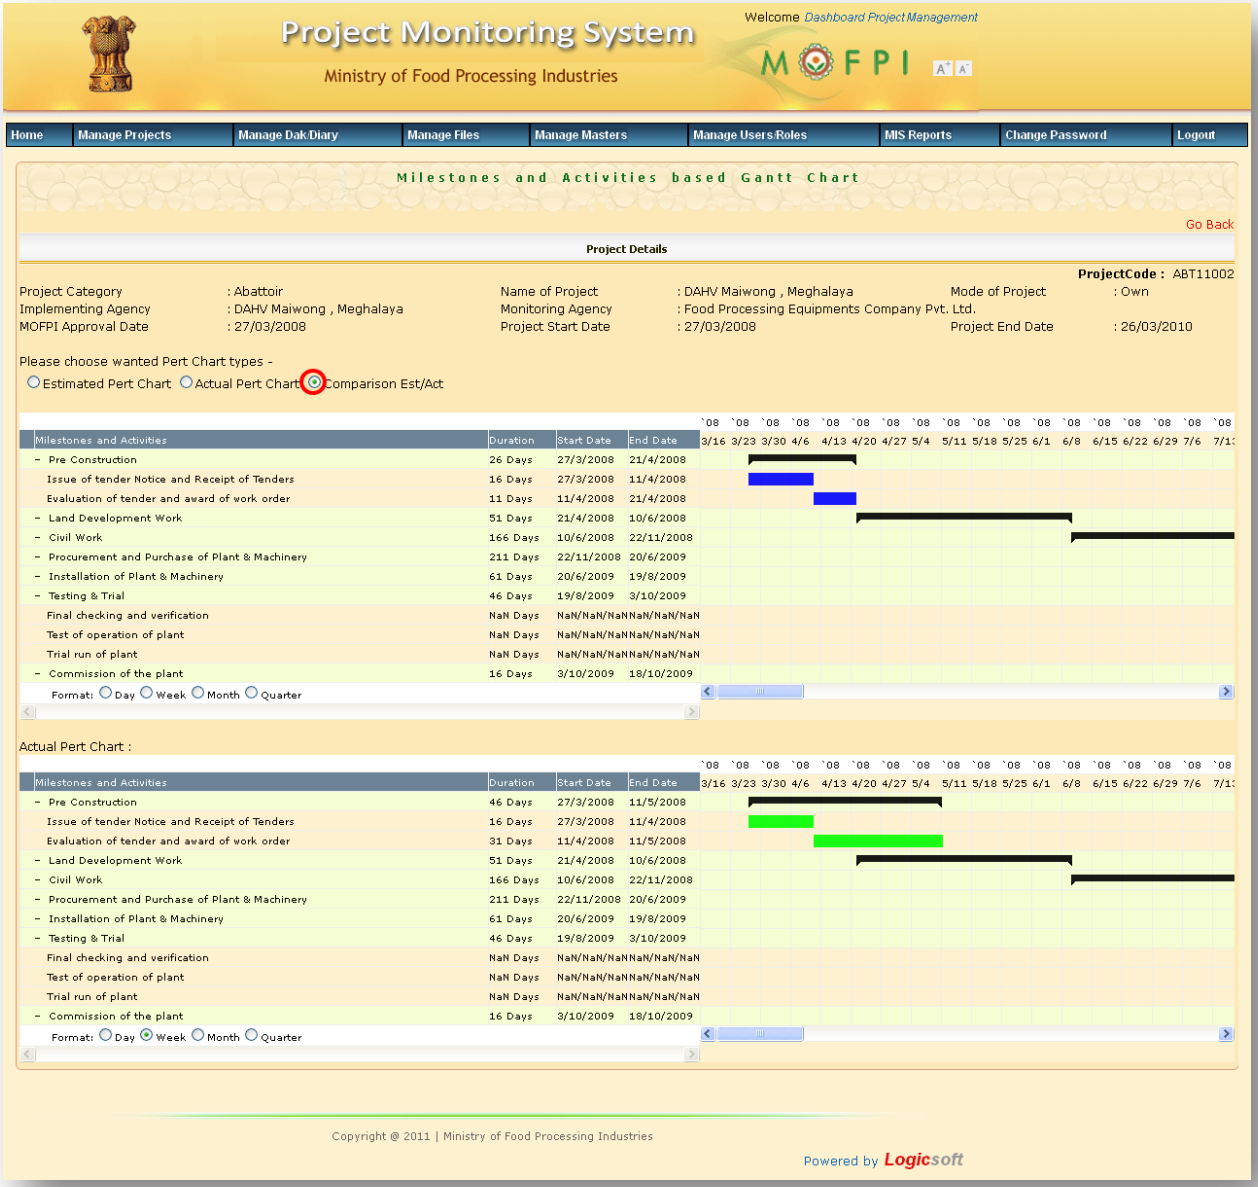
Project Monitoring System
Ministry of Food Processing Industries
Welcome Dashboard Project Management
MOFPI
Home
Manage Projects
Manage Dak/Diary
Manage Files
Manage Masters
Manage Users/Roles
MIS Reports
Change Password
Logout
Milestones and Activities based Gantt Chart
Go Back
Project Details
ProjectCode : ABT11002
Project Category : Abattoir
Implementing Agency : DAHV Maiwong , Meghalaya
MOFPI Approval Date : 27/03/2008
Name of Project : DAHV Maiwong , Meghalaya
Monitoring Agency : Food Processing Equipments Company Pvt. Ltd.
Project Start Date : 27/03/2008
Mode of Project : Own
Project End Date : 26/03/2010
Please choose wanted Pert Chart types -
Estimated Pert Chart
Actual Pert Chart
Comparison Est/Act
Milestones and Activities
Duration
Start Date
End Date
Pre Construction 26 Days 27/3/2008 21/4/2008
Issue of tender Notice and Receipt of Tenders 16 Days 27/3/2008 11/4/2008
Evaluation of tender and award of work order 11 Days 11/4/2008 21/4/2008
Land Development Work 51 Days 21/4/2008 10/6/2008
Civil Work 166 Days 10/6/2008 22/11/2008
Procurement and Purchase of Plant & Machinery 211 Days 22/11/2008 20/6/2009
Installation of Plant & Machinery 61 Days 20/6/2009 19/8/2009
Testing & Trial 46 Days 19/8/2009 3/10/2009
Final checking and verification NaN Days NaN/NaN/NaN NaN/NaN/NaN
Test of operation of plant NaN Days NaN/NaN/NaN NaN/NaN/NaN
Trial run of plant NaN Days NaN/NaN/NaN NaN/NaN/NaN
Commission of the plant 16 Days 3/10/2009 18/10/2009
Format: Day Week Month Quarter
Actual Pert Chart :
Pre Construction 46 Days 27/3/2008 11/5/2008
Issue of tender Notice and Receipt of Tenders 16 Days 27/3/2008 11/4/2008
Evaluation of tender and award of work order 31 Days 11/4/2008 11/5/2008
Land Development Work 51 Days 21/4/2008 10/6/2008
Civil Work 166 Days 10/6/2008 22/11/2008
Procurement and Purchase of Plant & Machinery 211 Days 22/11/2008 20/6/2009
Installation of Plant & Machinery 61 Days 20/6/2009 19/8/2009
Testing & Trial 46 Days 19/8/2009 3/10/2009
Final checking and verification NaN Days NaN/NaN/NaN NaN/NaN/NaN
Test of operation of plant NaN Days NaN/NaN/NaN NaN/NaN/NaN
Trial run of plant NaN Days NaN/NaN/NaN NaN/NaN/NaN
Commission of the plant 16 Days 3/10/2009 18/10/2009
Format: Day Week Month Quarter
Copyright @ 2011 | Ministry of Food Processing Industries
Powered by Logicsoft

With this chart, the user will get an overview of the estimated time allotted (based on prior experience) for an activity or milestone and the actual time that was required to complete the same activity.

Print Project Summary

To get the print copy of a project summary, Move the mouse over 'Manage Projects' and click on 'Projects'.

From the list of projects find the project that is to be printed.

Project Monitoring System
Ministry of Food Processing Industries
Welcome Dashboard Project Management
MOFPI
Home
Manage Projects
Manage Dak/Diary
Manage Files
Manage Masters
Manage Users/Roles
MIS Reports
Change Password
Logout
Projects Details
List of Project(s)
Search
Search Here
Auto search
Search
Add New Project
Project Name
Project Category
State
Total Project C
MOFPI Assista
Statu
Action
Shimla Municipal Corporation Abattoir Himachal Pradesh 196600000.0 114200000.0
DAHV Maiwong , Meghalaya Abattoir Meghalaya 207715000.0 150000000.0
Kolkata Municipal Corporation Abattoir West Bengal 2845000.00 1287340.00
Greater Hyderabad Municipal Corporation Abattoir Andhra Pradesh 3284000.00 1478980.00
Patna Municipal Corporation Abattoir Bihar 2638000.00 1097210.00
Dimapur Municipal Council Abattoir Nagaland 2288000.00 143750.00
Jammu Municipal Corporation Abattoir Jammu & Kashmir 2300000.00 150000.00
Ranchi Municipal Corporation Abattoir Jharkhand 186678000.0 86459500.00
Ahmednagar Dist Goat Rearing & Processing Co Abattoir Maharastra 235200000.0 85102000.00
North East Mega Food Park Ltd. Mega Food Parks Assam 759800000.0 500000000.0
Records per page: 10
Records: 1 - 10 of 48 - Pages: 1 | 2 | 3 | 4 | 5
Go to page
Copyright @ 2011 | Ministry of Food Processing Industries
Powered by Logicsoft

SMS and Email Communication

To send communication related to a project through SMS or e-mail, Move the mouse over ‘Manage Projects’ and click on ‘Projects’.

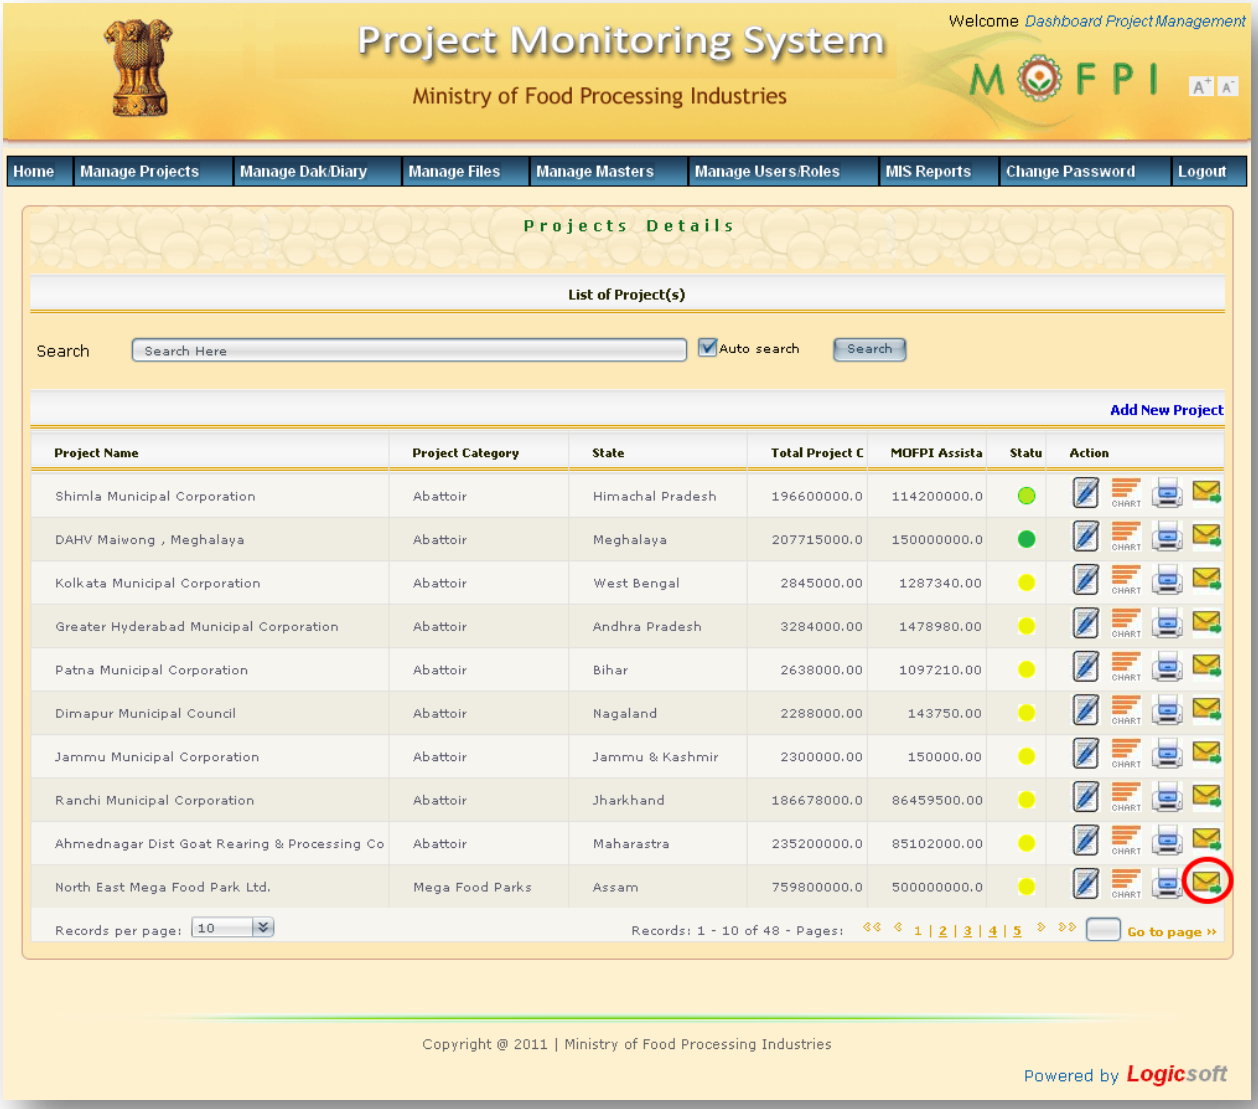

From the list of projects find the project and click on the communication link.

Click on ‘Send via SMS’ or ‘Send via Email’ link to find the communication page.

Send via SMS

Select the agency name, enter the mobile number. After writing the message send the SMS.

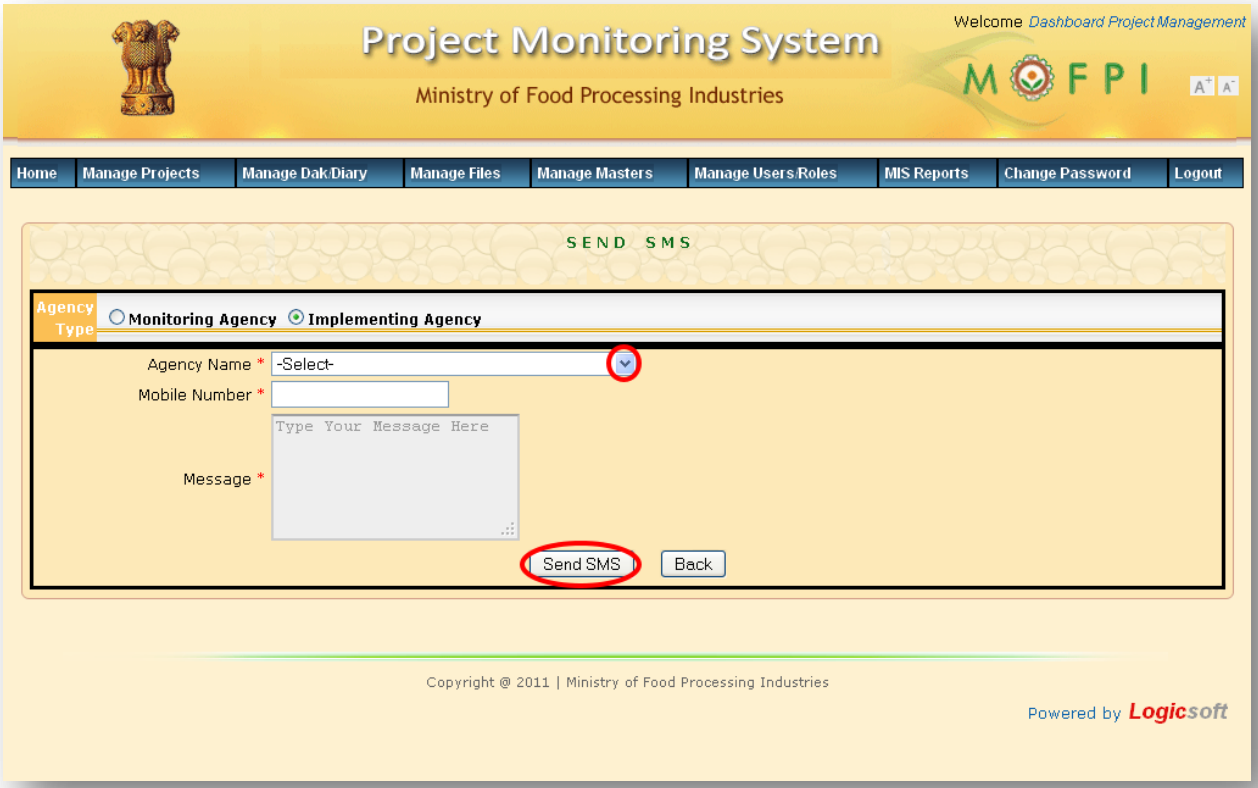

Send via Email



In the similar way send Email communication to the concerned person.

Manage Masters

All the details like scheme type; milestone etc useful while adding a new project can be managed using this module.

Scheme Type

List of Scheme Types and Actions for each scheme

For each scheme type in the list there are edit, delete and change status options as shown in the screen.

Click on 'Change Status' for any Scheme type and confirm the message to change the status of the scheme from active to Inactive or vice versa.

The Scheme types with inactive status will not be listed in the scheme type drop down box in the new project (application) form.

Modify and update the scheme details using the edit option.

Delete any scheme type, if it is not required further.

Project Monitoring System
Ministry of Food Processing Industries
Welcome Dashboard Project Management
MOFPI
Home
Manage Projects
Manage Dak/Diary
Manage Files
Manage Masters
Manage Users/Roles
MIS Reports
Change Password
Logout
Scheme Types
Add New Project Scheme
List of Project Scheme
S.No.
Project Category Name
Description
Status
Action
1. Abattoir Abattoir Active Change Status / Edit / Delete
2. Cold Chain Cold Chain Active Change Status / Edit / Delete
3. Labs Labs Active Change Status / Edit / Delete
4. Mega Food Parks Mega Food Parks Active Change Status / Edit / Delete
5. Research and Development Research and Development Active Change Status / Edit / Delete
Copyright @ 2011 | Ministry of Food Processing Industries
Powered by Logicsoft

Add New Scheme Type:-

A new scheme type can be added using this option.

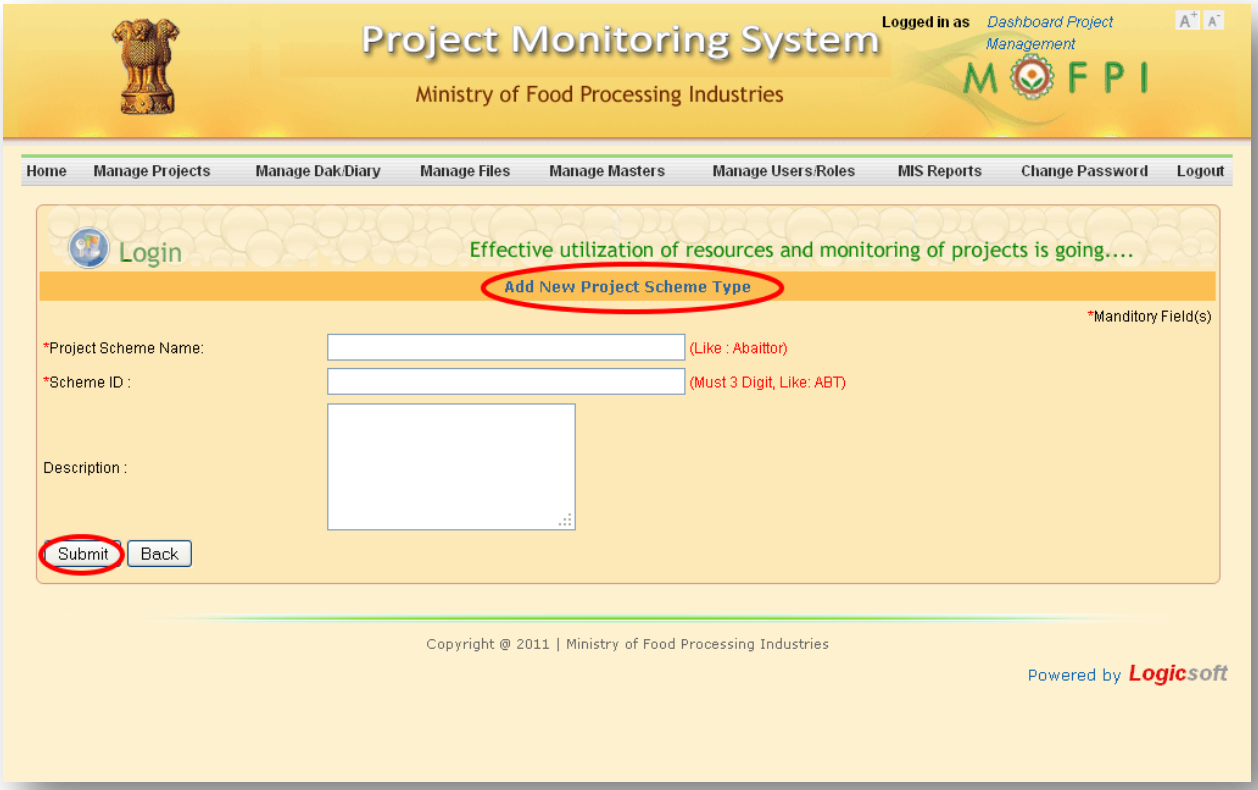

Enter the Project Scheme Name, Scheme ID, description and submit the form to save the details.

The added scheme type will be saved in the database and can be seen while adding a new project (in the scheme type drop down box).

Milestone(s)

The list of all milestones under each scheme type will be displayed as shown in the screen below.

Using the change status, edit and delete option available for each Milestone, the status can be changed or updated or deleted from the list.

Ministry of Food Processing Industries
Home
Manage Projects
Manage Dak/Diary
Manage Files
Manage Masters
Manage Users/Roles
MIS Reports
Change Password
Logout
Milestone Details
Search Milestone(s)
Scheme Type :
All
Milestone Name :
Search
Reset
List of Milestone :
Add New Milestone
Abattoir
S.No.
Milestone Name
Description
Status
Action
1. Pre Construction - Change Status / Edit / Delete
2. Land Development Work - Change Status / Edit / Delete
3. Civil Work - Change Status / Edit / Delete
4. Procurement and Purchase of Plant & Machinery - Change Status / Edit / Delete
5. Installation of Plant & Machinery - Change Status / Edit / Delete
6. Testing & Trial - Change Status / Edit / Delete
7. Commission of the plant - Change Status / Edit / Delete
Mega Food Parks

Add New Mile stone

A milestone can be added under any scheme type as explained in the following section.

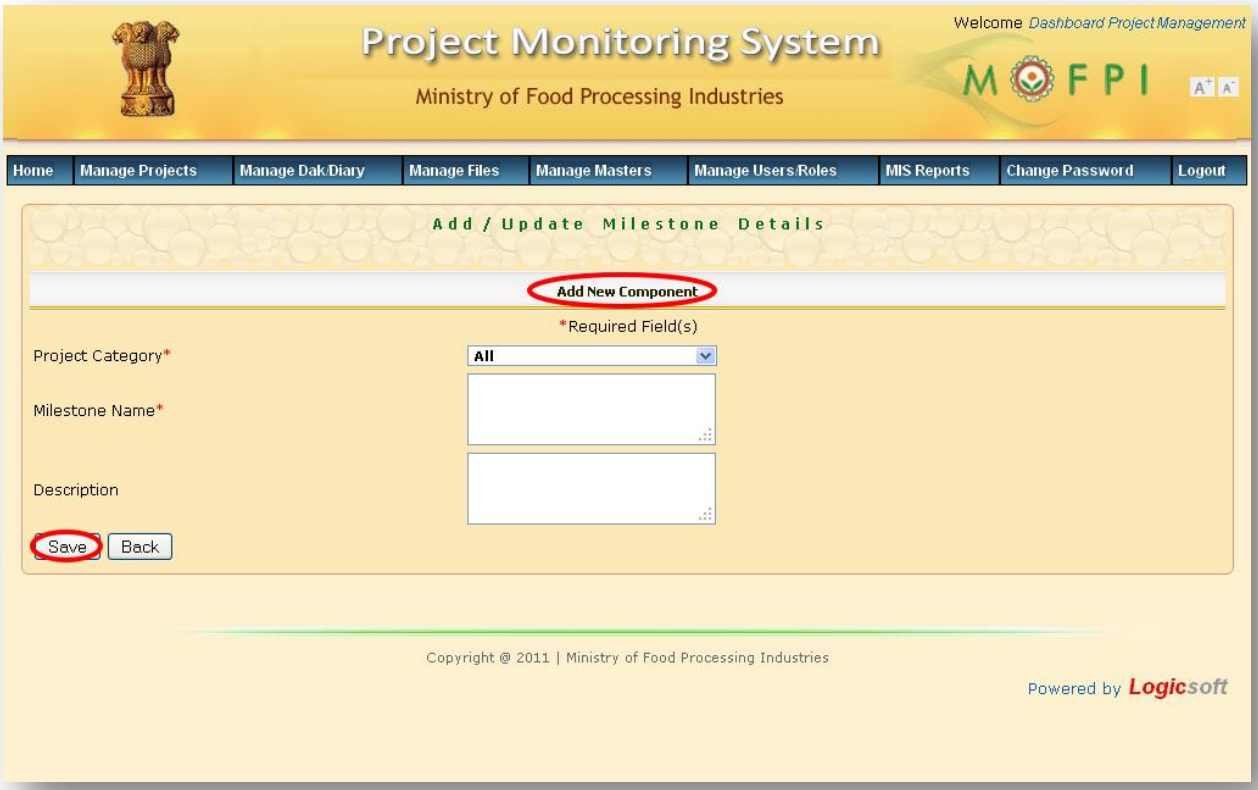

Select the Project Category (Scheme type) from the drop down list and enter the Milestone name and description and save it.

Milestone- Activities

The list of all milestone activities under each Milestone will be displayed as shown in the screen below.

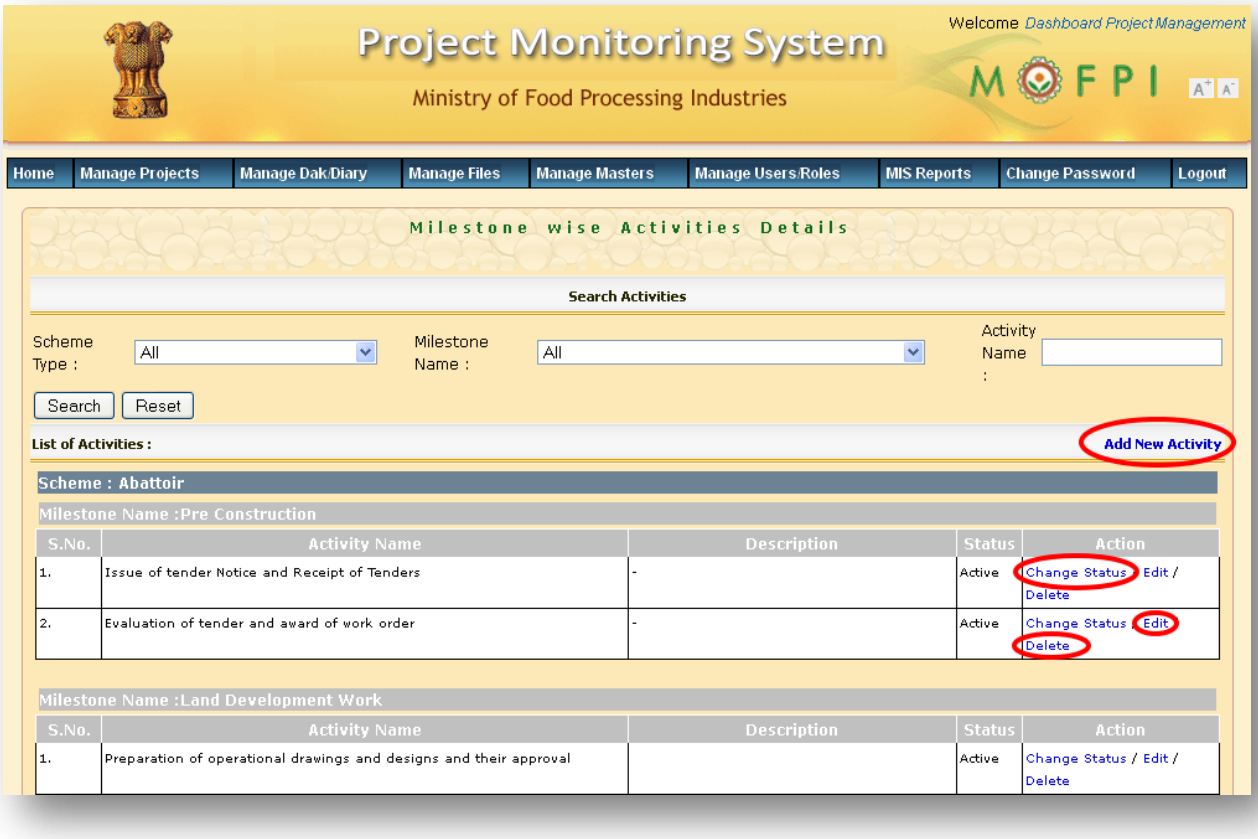

Using the change status, edit and delete option available for each activity, the status can be changed or updated or deleted from the list.

Click on 'Add New Activity'.

Add New Mile stone-Activity

A milestone activity can be added under any Milestone as explained in the following section.

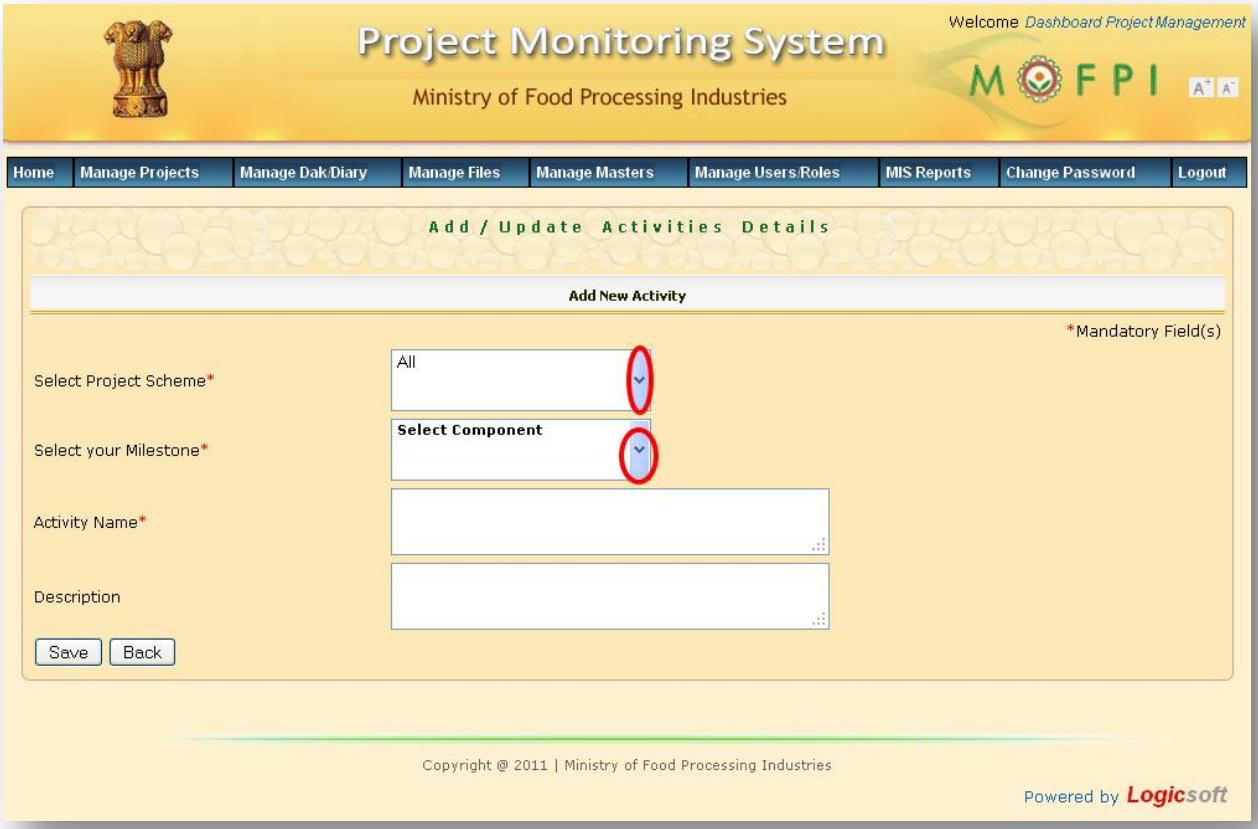

Select the Project Scheme type (scheme) and milestone from the respective drop down fields and enter the Activity name and description and save it.

Monitoring Agency

List of Monitoring Agencies:-

The list of all Monitoring agencies will be displayed as shown in the screen below.

Using the change status, edit and delete option available for each Monitoring agency, the status can be changed or updated or deleted from the list.

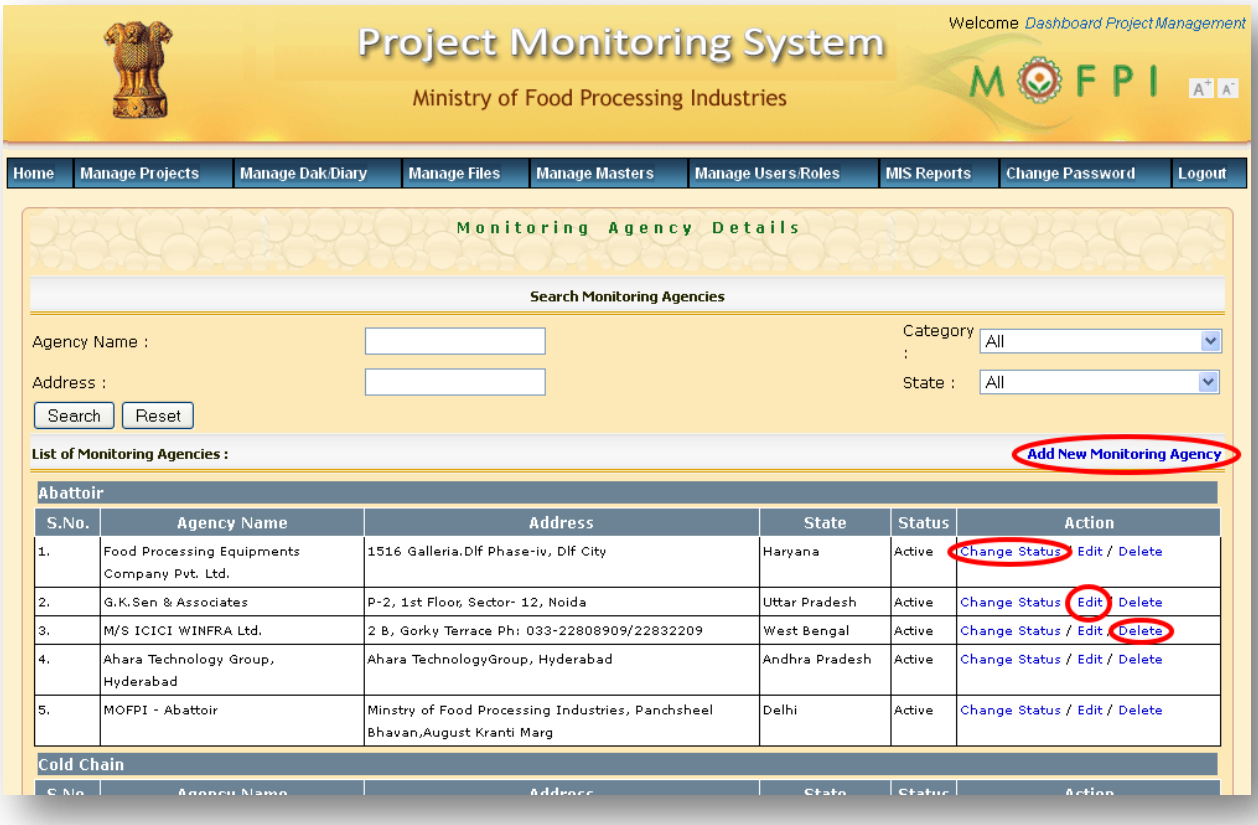
Project Monitoring System
Ministry of Food Processing Industries
Welcome Dashboard Project Management
MOFPI
Home
Manage Projects
Manage Dak/Diary
Manage Files
Manage Masters
Manage Users/Roles
MIS Reports
Change Password
Logout
Monitoring Agency Details
Search Monitoring Agencies
Agency Name :
Category :
All
Address :
State :
All
Search
Reset
List of Monitoring Agencies :
Add New Monitoring Agency
Abattoir
S.No.
Agency Name
Address
State
Status
Action
1. Food Processing Equipments Company Pvt. Ltd. 1516 Galleria.Dlf Phase-iv, Dlf City Haryana Active Change Status / Edit / Delete
2. G.K.Sen & Associates P-2, 1st Floor, Sector- 12, Noida Uttar Pradesh Active Change Status / Edit / Delete
3. M/S ICICI WINFRA Ltd. 2 B, Gorky Terrace Ph: 033-22808909/22832209 West Bengal Active Change Status / Edit / Delete
4. Ahara Technology Group, Hyderabad Ahara TechnologyGroup, Hyderabad Andhra Pradesh Active Change Status / Edit / Delete
5. MOFPI - Abattoir Minstry of Food Processing Industries, Panchsheel Bhavan,August Kranti Marg Delhi Active Change Status / Edit / Delete
Cold Chain

Click on ‘Add New Monitoring Agency’.

Add New Monitoring Agency

1.) Project Category: - From the drop down box select the required project category.

2.) **User ID: -** Enter the user id.

3.) Name of Agency: - Enter agency name.

4.) **Address: -** Enter the Monitoring agency address.

5.) State: - Select the state from the drop down box.

6.) City: - The cities in the selected state will be listed. Select the city from the drop down field.

7.) Pin Code: - Enter the Pin code of the place.

8.) Establishment Date: - Select the company establishment date from the calendar.

9.) Contact person: - Enter the contact person's name.

10.) Contact Number: - Enter the telephone number.

11.) Email ID: - Enter the email id.

12.) License number: - Enter the License number.

13.) License Issued Date: - Select the License Issued Date from the calendar.

14.) License expiry Date: - Select the License expiry Date from the calendar.

Save the details.

List of Implementing Agencies:-

The list of all implementing agencies will be displayed as shown in the screen below.

Using the change status, edit and delete option available for each implementing agency, the status can be changed or updated or deleted from the list.

Click on ‘Add New Implementing Agency’.

Add New Implementing Agency

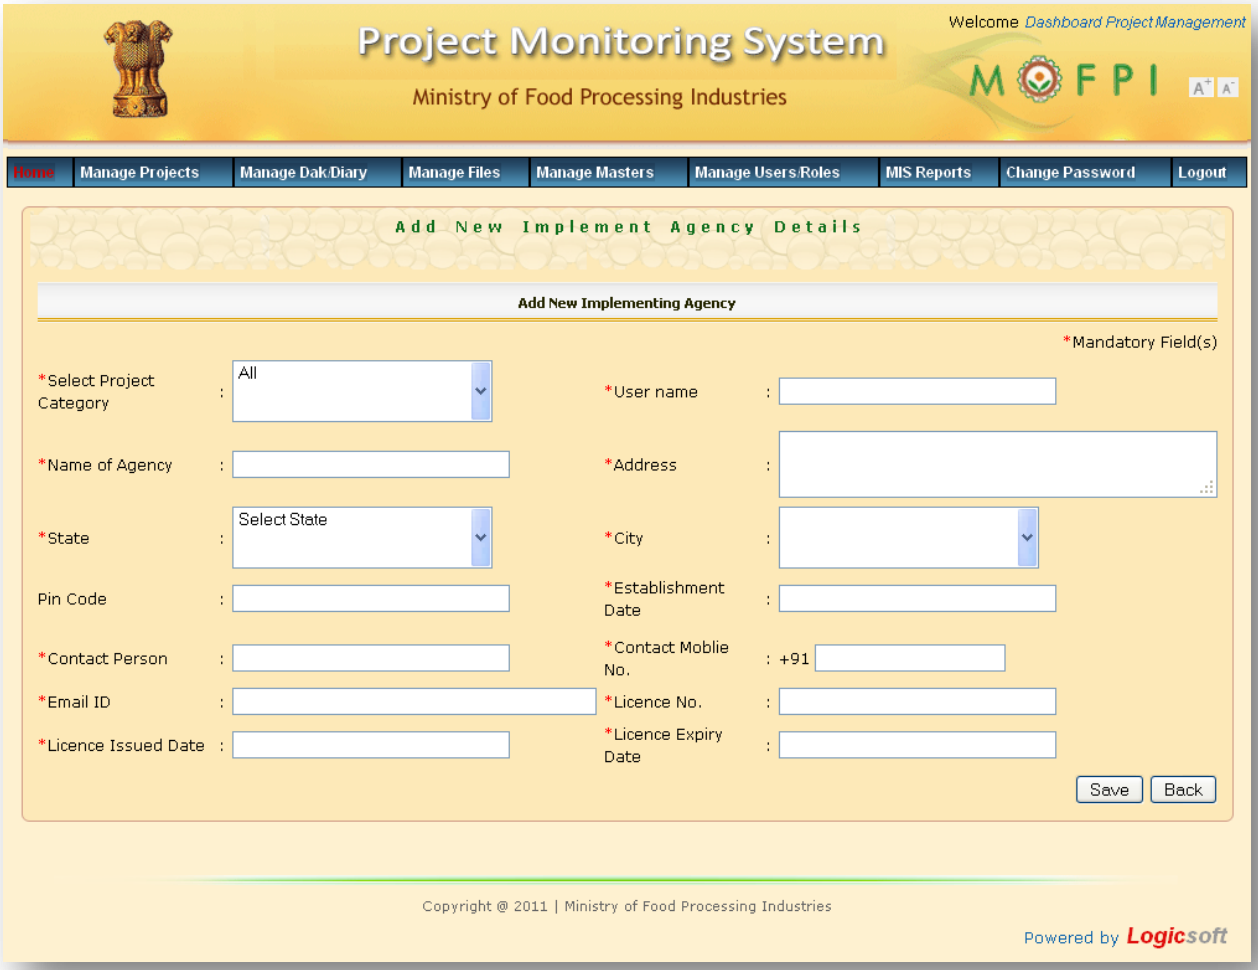

1.) Select Project Category: - From the drop down box select the required project category.

2.) **User Name: -** Enter the user name.

3.) Name of Agency: - Enter agency name.

4.) **Address: -** Enter the Implementing agency address.

5.) State: - Select the state from the drop down box.

6.) City: - The cities in the selected state will be listed. Select the city from the drop down field.

7.) Pin Code: - Enter the Pin code of the place.

8.) Establishment Date: - Select the establishment date from the calendar.

9.) Contact person: - Enter the contact person's name.

10.) Contact Mobile Number: - Enter the telephone number.

11.) Email ID: - Enter the email id.

12.) License number: - Enter the License number.

13.) License Issued Date: - Select the License Issued Date from the calendar.

14.) License expiry Date: - Select the License expiry Date from the calendar.
